PROJECT RAMPART PROGRAMME DASHBOARD ◆ ILLUSTRATIVE — EXAMPLE GROUP

Reporting is on track; market access is the binding constraint

The weekly management view for the executive sponsor and Steering Committee of the EU Cyber Resilience Act readiness programme. Status as at 30 Oct 2026 (SteerCo #1). Example Group is a fictional client and every client figure is illustrative.

KPIs · Readiness · Market access · Delivery · Money · Risk and decisions

OVERALL PROGRAMME STATUS

◆ Amber

Reporting capability on track; market access at risk because no CRA notified body was designated at checks to 8 Sep 2026 (external dependency).

Next decision point: the board on 19 Nov 2026 (asks BD1–BD5 below).

COUNTDOWN

406

days to full application of the CRA on **11 Dec 2027**

Counted from pack issue on 31 Oct 2026; 387 days from the board.

ARTICLE 14 REPORTING

Live since 11 Sep 2026

An early warning is due within **24** hours for every in-scope product, including those already on the market.

First drill filed its early warning in 9h 40m.

ILLUSTRATIVE ENGAGEMENT

Example Group

Fictional maker of connected products: EUR 1.2bn revenue, 13 product families and 55 SKUs in scope.

Client data as at 30 Oct 2026; regulatory facts verified to 30 Oct 2026 (notified-body count: checks to 8 Sep 2026).

— KPIS

Reporting KPIs are Green; signed SBOM coverage is the KPI in Red

5 Green · **6** Amber · **1** Red across the SteerCo KPI pack

READINESS AND SCOPE

K01 ◆ Amber

Portfolio readiness index

44%

Target 70% by Jun 2027; 90% by Nov 2027
Trend Baseline

Source: Readiness diagnostic, 28 Oct 2026 · Illustrative

K02 ◆ Amber

Families with final scope and class decision

11 / 13

Target 13 / 13 by 18 Dec 2026
Trend New

Source: Scope register · Illustrative

K03 ◆ Amber

Class I/II families with route and notified-body plan

5 / 7

Target 7 / 7 by 19 Nov 2026
Trend New

Source: Scope register · Illustrative

ARTICLE 14 REPORTING

K04 ● Green

SRP Assigned Representatives registered

3

Target ≥ 2 at all times
Trend Stable

Source: SRP roster · Illustrative

K05 ● Green

Art 14 drill: time to early warning

9h 40m

Target < 24h incl. weekends
Trend First drill

Source: Drill record 22 Oct 2026 · Illustrative

K06 ● Green

Art 14 cases assessed (reportable / not reportable)

0 / 4

Target 100% decided with UTC timeline
Trend Stable

Source: PSIRT case files · Illustrative

ENGINEERING AND SUPPLY CHAIN

K07 ■ Red

Releases with signed SBOM (last 30 days)

38% (9 / 24)

Target 100% by 31 Mar 2027
Trend Up from 21%

Source: Build pipeline · Illustrative

K08 ● Green

Families with signed risk assessment

0 / 13 (T200 in review)

Target Wave 1 (8) by 26 Feb 2027
Trend On plan

Source: System of record · Illustrative

K09 ◆ Amber

In-scope suppliers on CRA clauses

6 / 41 (15%)

Target Top 15 by Jan 2027; all by Jun 2027
Trend New

Source: Contract register · Illustrative

PEOPLE, MONEY AND MARKET ACCESS

K10 ◆ Amber

Engineers trained

140 / 920 (15%)

Target 60% by Mar 2027
Trend Up

Source: LMS · Illustrative

K11 ● Green

Spend to date vs plan

EUR 0.41m vs EUR 0.38m

Target Within ±10% of plan
Period Oct 2026

Source: Finance · Illustrative

K12 ◆ Amber

Notified-body candidates

3 shortlisted; 1 proposal

Target 3 pre-assessments contracted by 29 Jan 2027
Trend New

Source: Programme · Illustrative

— READINESS

Readiness is 44% and must reach 93% by Dec 2027; conformity is weakest at 16%

Class I home products are least ready at **37%** (L2 **35%**, V1 **38%**). By business unit: Home & Building Solutions **39%**, Industrial Connectivity **52%**, Software & Services **41%**. Art 14 reporting is the strongest domain at **72%**.

Portfolio readiness index: plan and actual

Average question score, capped at level 3 and shown as a share of level 3. Baseline self-assessed by product teams and moderated by the programme.

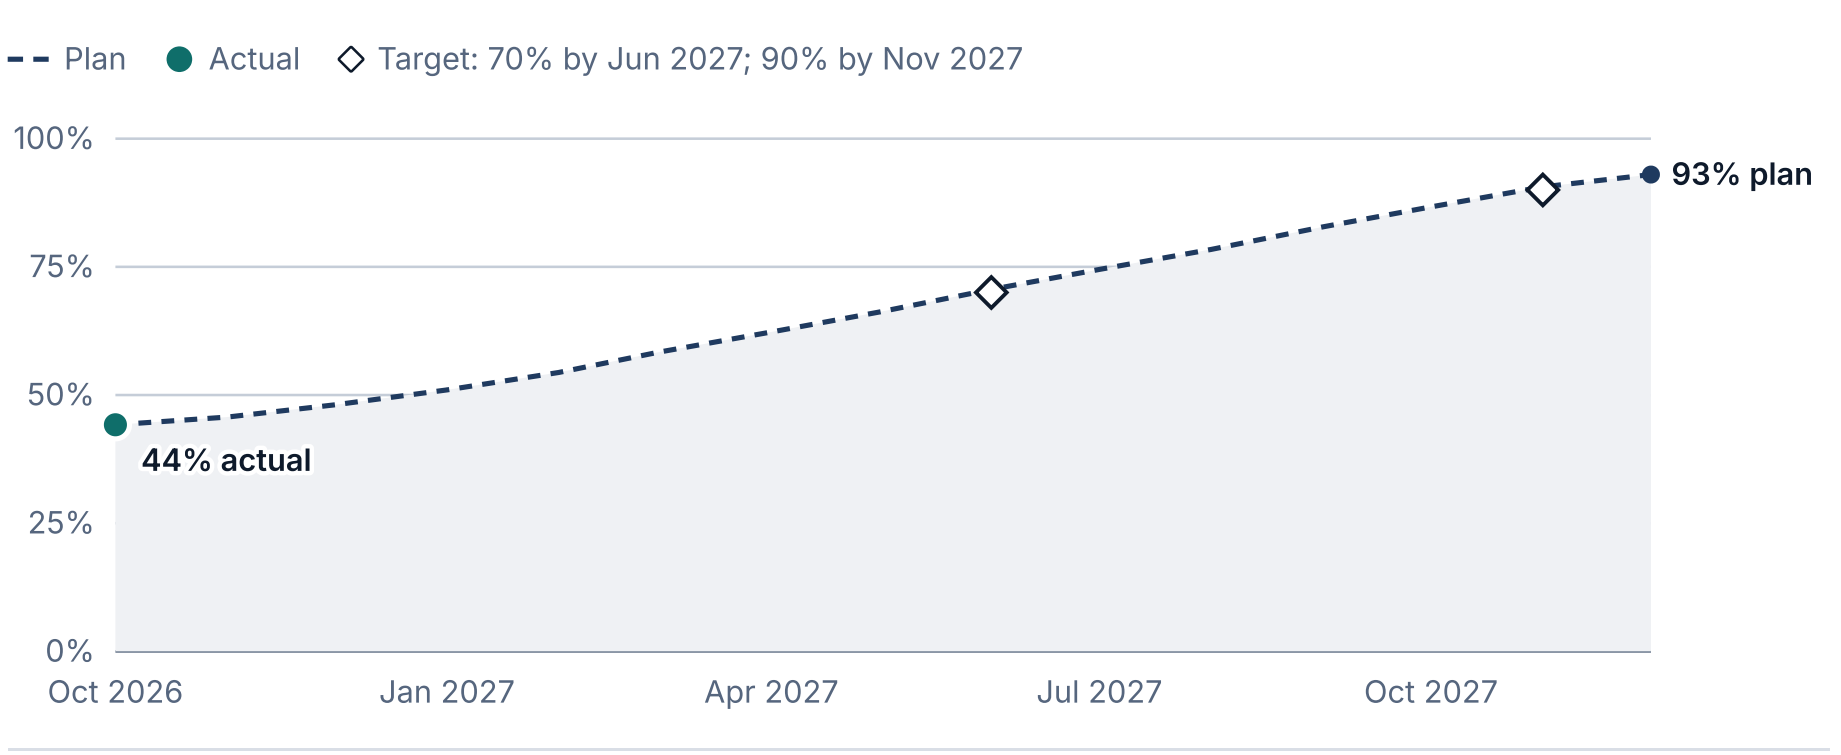

Source: Readiness diagnostic, 28 Oct 2026 (actual); programme plan (trajectory and targets) · Illustrative

Signed SBOM coverage: plan and actual

Releases with signed SBOM (last 30 days). Target: 100% by 31 Mar 2027.

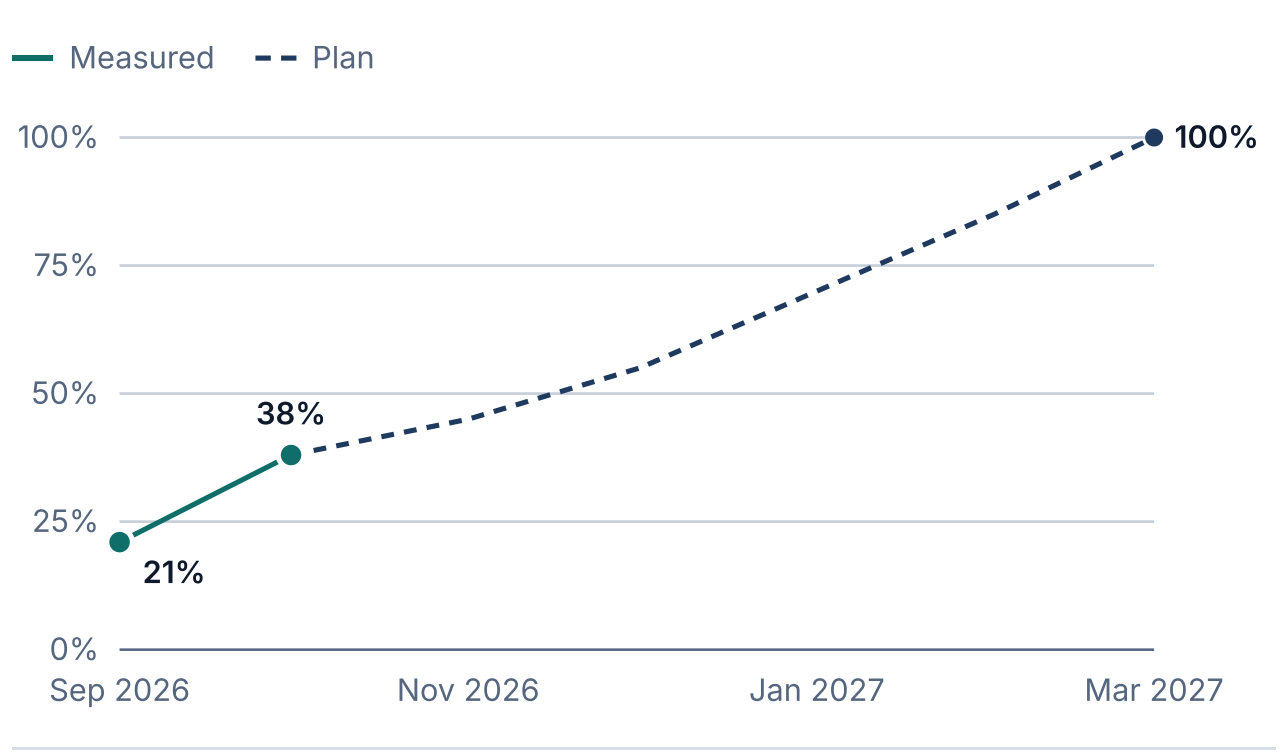

Source: Build pipeline; Sep 2026 is the pre-programme measurement · Illustrative

Readiness by diagnostic domain

Ranked. Dashed line: the Jun 2027 portfolio target of 70%.

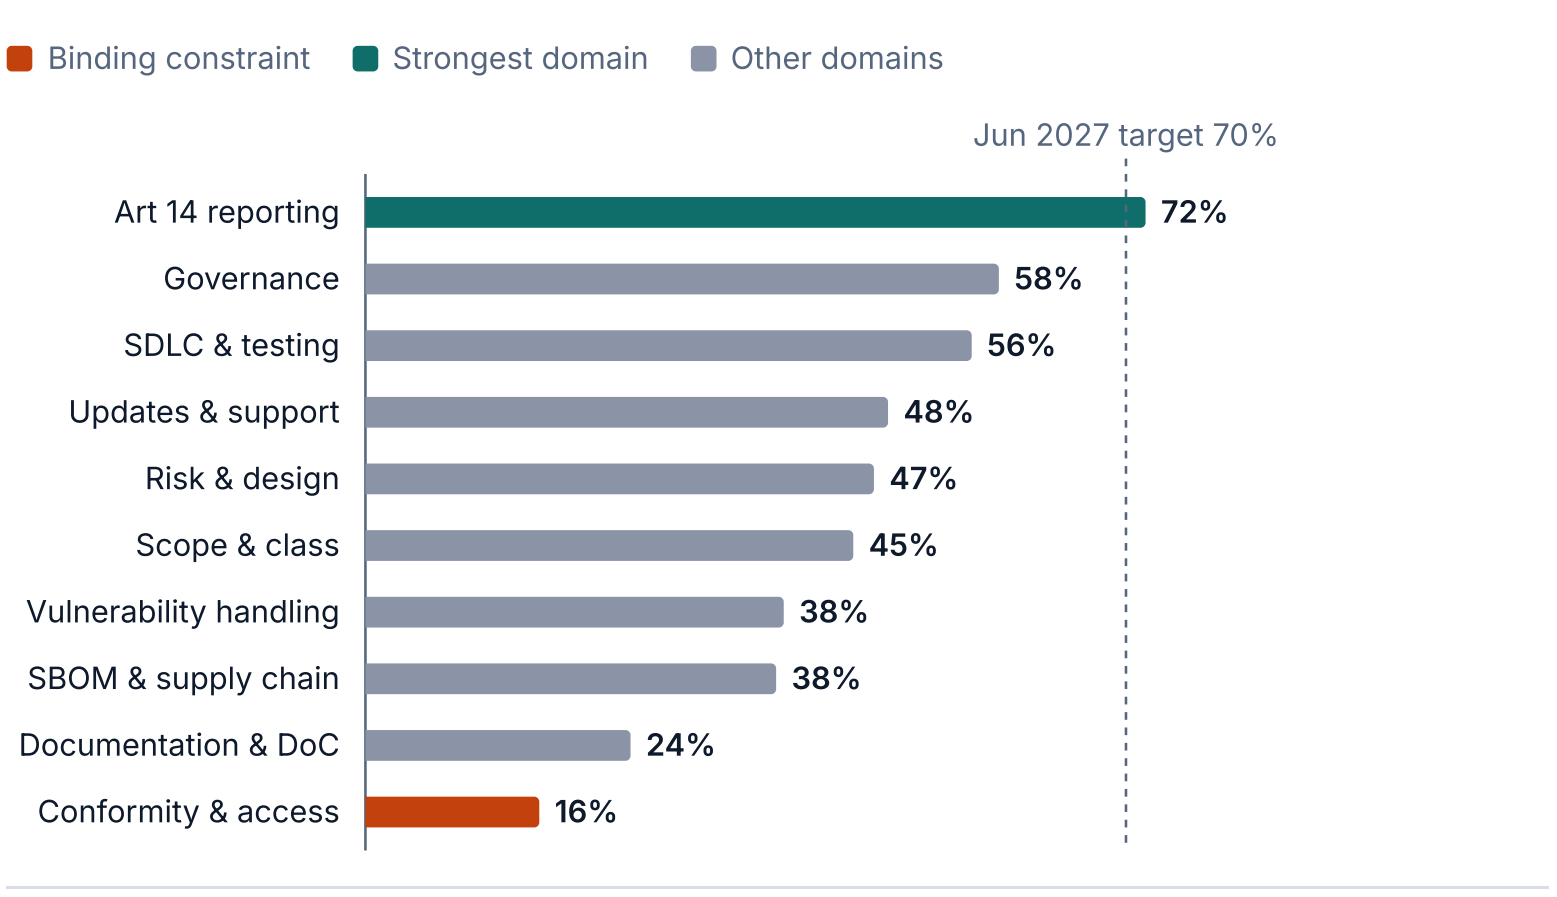

Source: Readiness diagnostic, 28 Oct 2026 · Illustrative

Readiness by product family

Ranked; colour shows CRA class. Dashed line: portfolio index of 44%.

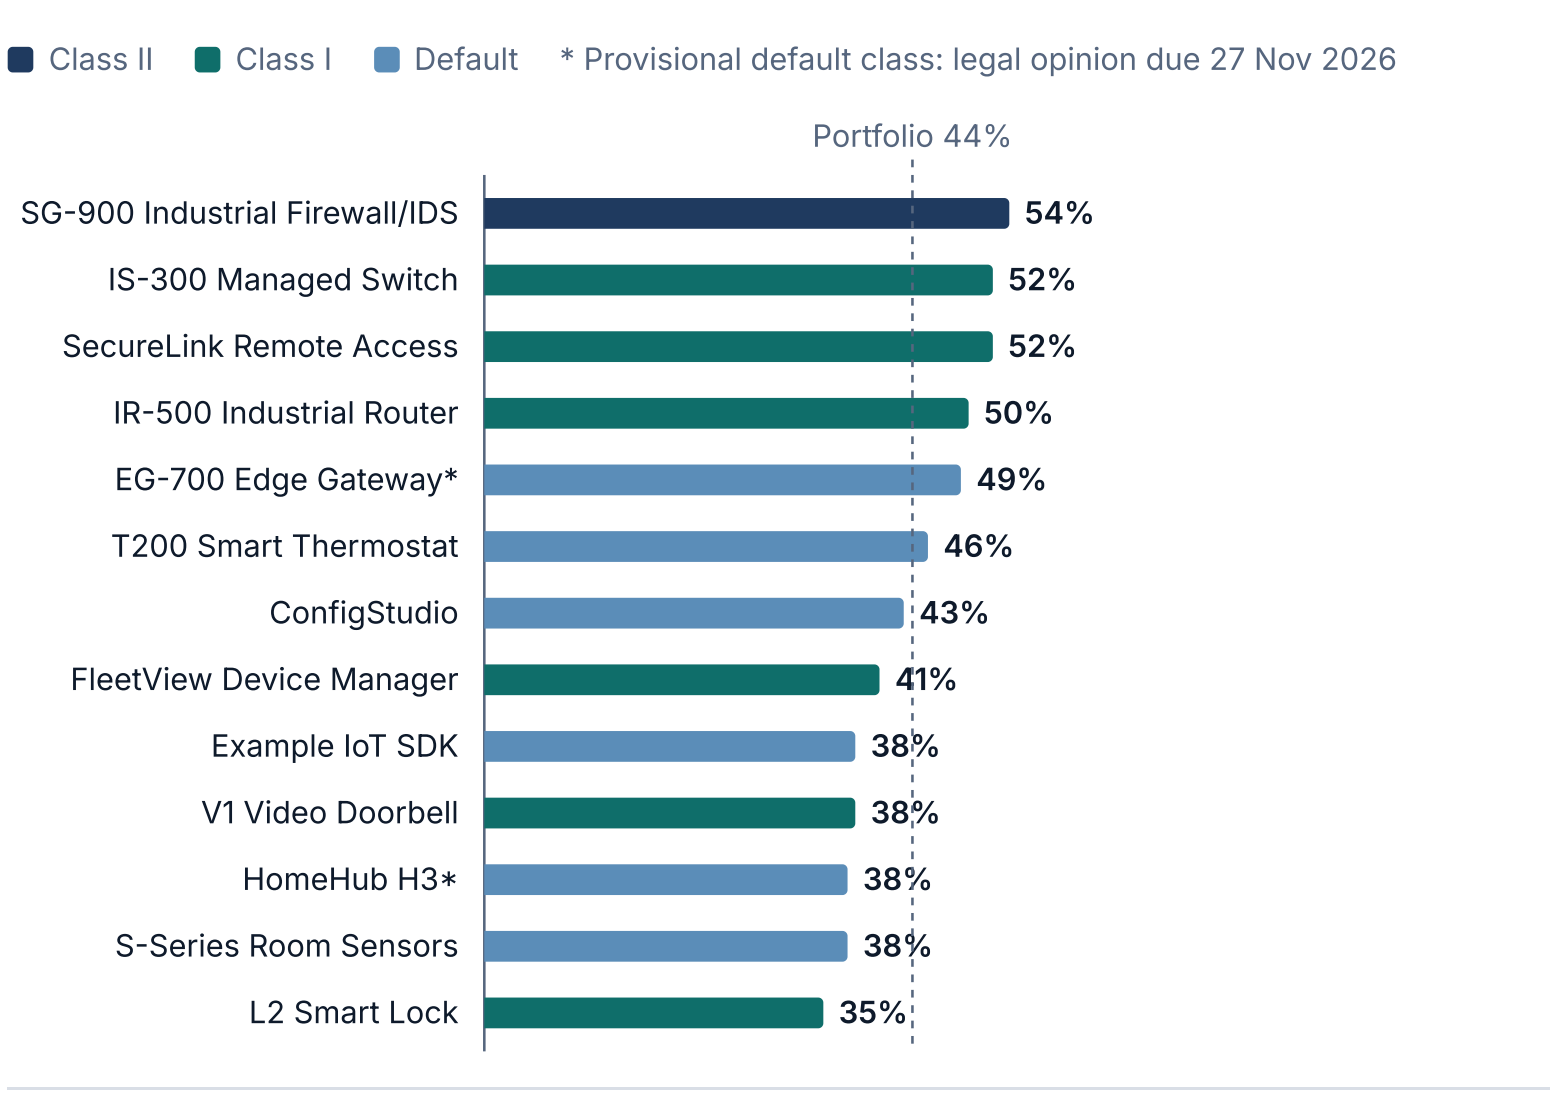

Source: Readiness diagnostic, 28 Oct 2026; scope register · Illustrative

— MARKET ACCESS ■ BINDING CONSTRAINT

EUR 468m of EU revenue needs a notified body; none was verifiably designated at checks to 8 Sep 2026

7 of **13** product families are Class I or Class II. Class II always needs a notified body, and Class I needs one until a harmonised standard is cited, so each of them needs an assessment slot before full application on 11 Dec 2027.

EU revenue by CRA class

EUR 468m sits in Class I and Class II families and needs a notified body: **39%** of group revenue.

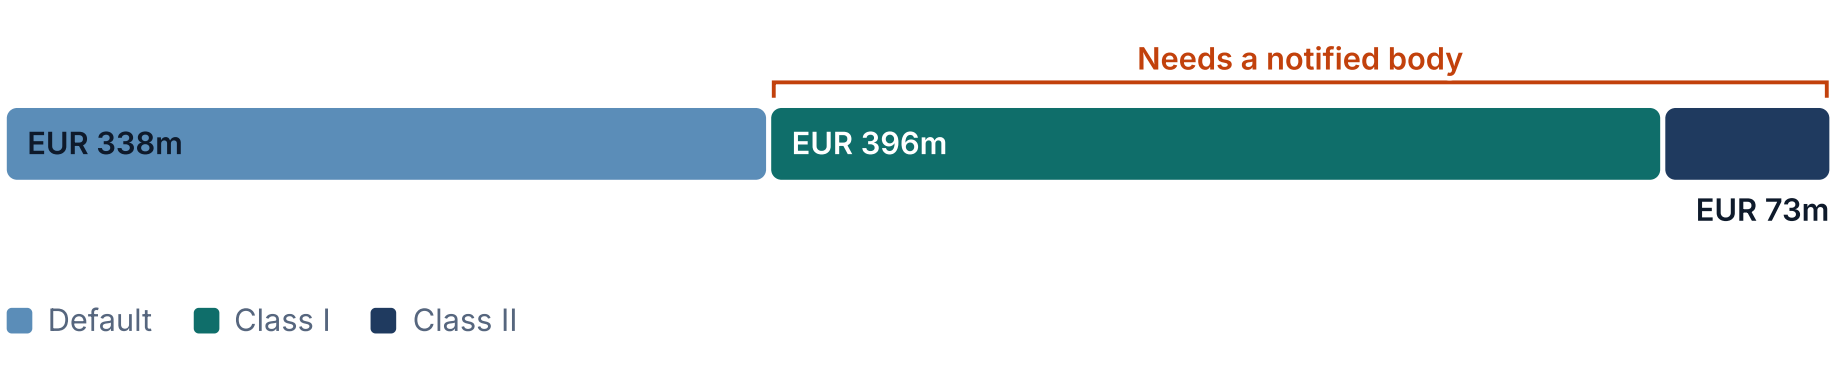

CRA class	Families	EU revenue (EUR m)	Group revenue (EUR m)	Needs a notified body
Default	6	338.3	475	No
Class I	6	395.7	585	Yes
Class II	1	72.6	110	Yes

Covers the in-scope product families. Legacy lines still sold in the EU (IR-300 and IS-200, EUR 18m of EU revenue) are excluded; board ask BD5 proposes their withdrawal.

Source: Finance; scope register · Illustrative

Notified-body readiness

External capacity is the dependency the programme cannot build itself.

CRA notified bodies verifiably designated (NANDO, checks to 8 Sep 2026) **0**

No CRA notified body was verifiably designated in NANDO at checks to 8 Sep 2026; Member States must 'strive' for enough bodies by 11 Dec 2026.

Harmonised standards cited in the Official Journal **0**

No harmonised standard is cited in the OJ and no common specification is adopted (30 Oct 2026); Class I products cannot use Module A until one is cited and applied in full.

Candidate notified bodies (K12) **3 shortlisted; 1 proposal**

Target: 3 pre-assessments contracted by 29 Jan 2027.

Pre-assessments contracted (M5) **29 Jan 2027**

◆ At risk

Formal engagements contracted (M7) **31 Mar 2027**

◆ At risk

Source: NANDO and Single Market Compliance Space: no CRA notified body verifiably designated (checks to 8 Sep 2026); Official Journal: no harmonised standard cited (30 Oct 2026); SteerCo #1 KPI pack and programme plan · Illustrative

Conformity route by product family

Module A: internal control (self-assessment). Module B+C: EU-type examination by a notified body. Module H: full quality assurance approved by a notified body. Families that need a notified body are listed first.

Family	BU	CRA class	Route	Wave	EU revenue (EUR m)	Support (years)	Readiness
IR-500 Industrial Router	IC	Class I	Module H	Wave 1	108.9	12	50%
IS-300 Managed Switch	IC	Class I	Module H	Wave 1	79.2	12	52%
V1 Video Doorbell	HBS	Class I	Module B+C	Wave 1	74.0	7	38%
SG-900 Industrial Firewall/IDS	IC	Class II	Module H	Wave 1	72.6	10	54%
L2 Smart Lock	HBS	Class I	Module B+C	Wave 1	55.5	10	35%
SecureLink Remote Access	IC	Class I	Module H	Wave 1	46.2	7	52%
FleetView Device Manager	SS	Class I	Module H	Wave 1	31.9	5	41%
T200 Smart Thermostat	HBS	Default	Module A	Wave 1 (pilot)	125.8	10	46%
HomeHub H3	HBS	Default (provisional)	Module A (B+C if Class I)	Wave 2	70.3	7	38%
EG-700 Edge Gateway	IC	Default (provisional)	Module A (H if Class I)	Wave 2	62.7	10	49%
S-Series Room Sensors	HBS	Default	Module A	Wave 2	59.2	8	38%
Example IoT SDK	SS	Default	Module A	Wave 2	11.6	5	38%
ConfigStudio	SS	Default	Module A	Wave 2	8.7	5	43%

Source: Scope register; Finance; Readiness diagnostic, 28 Oct 2026 · Illustrative

— DELIVERY

3 milestones are at risk: notified-body contracting and the SBOM pipeline

Workstreams: **2** Green, **4** Amber, **2** Red. Reporting readiness (P0) is complete; inventory, scope and classification (P1) runs to 18 Dec 2026.

Phases and milestones

Bars are phase windows; diamonds are milestones; the vertical line is the data date. Hover or focus a mark for detail.

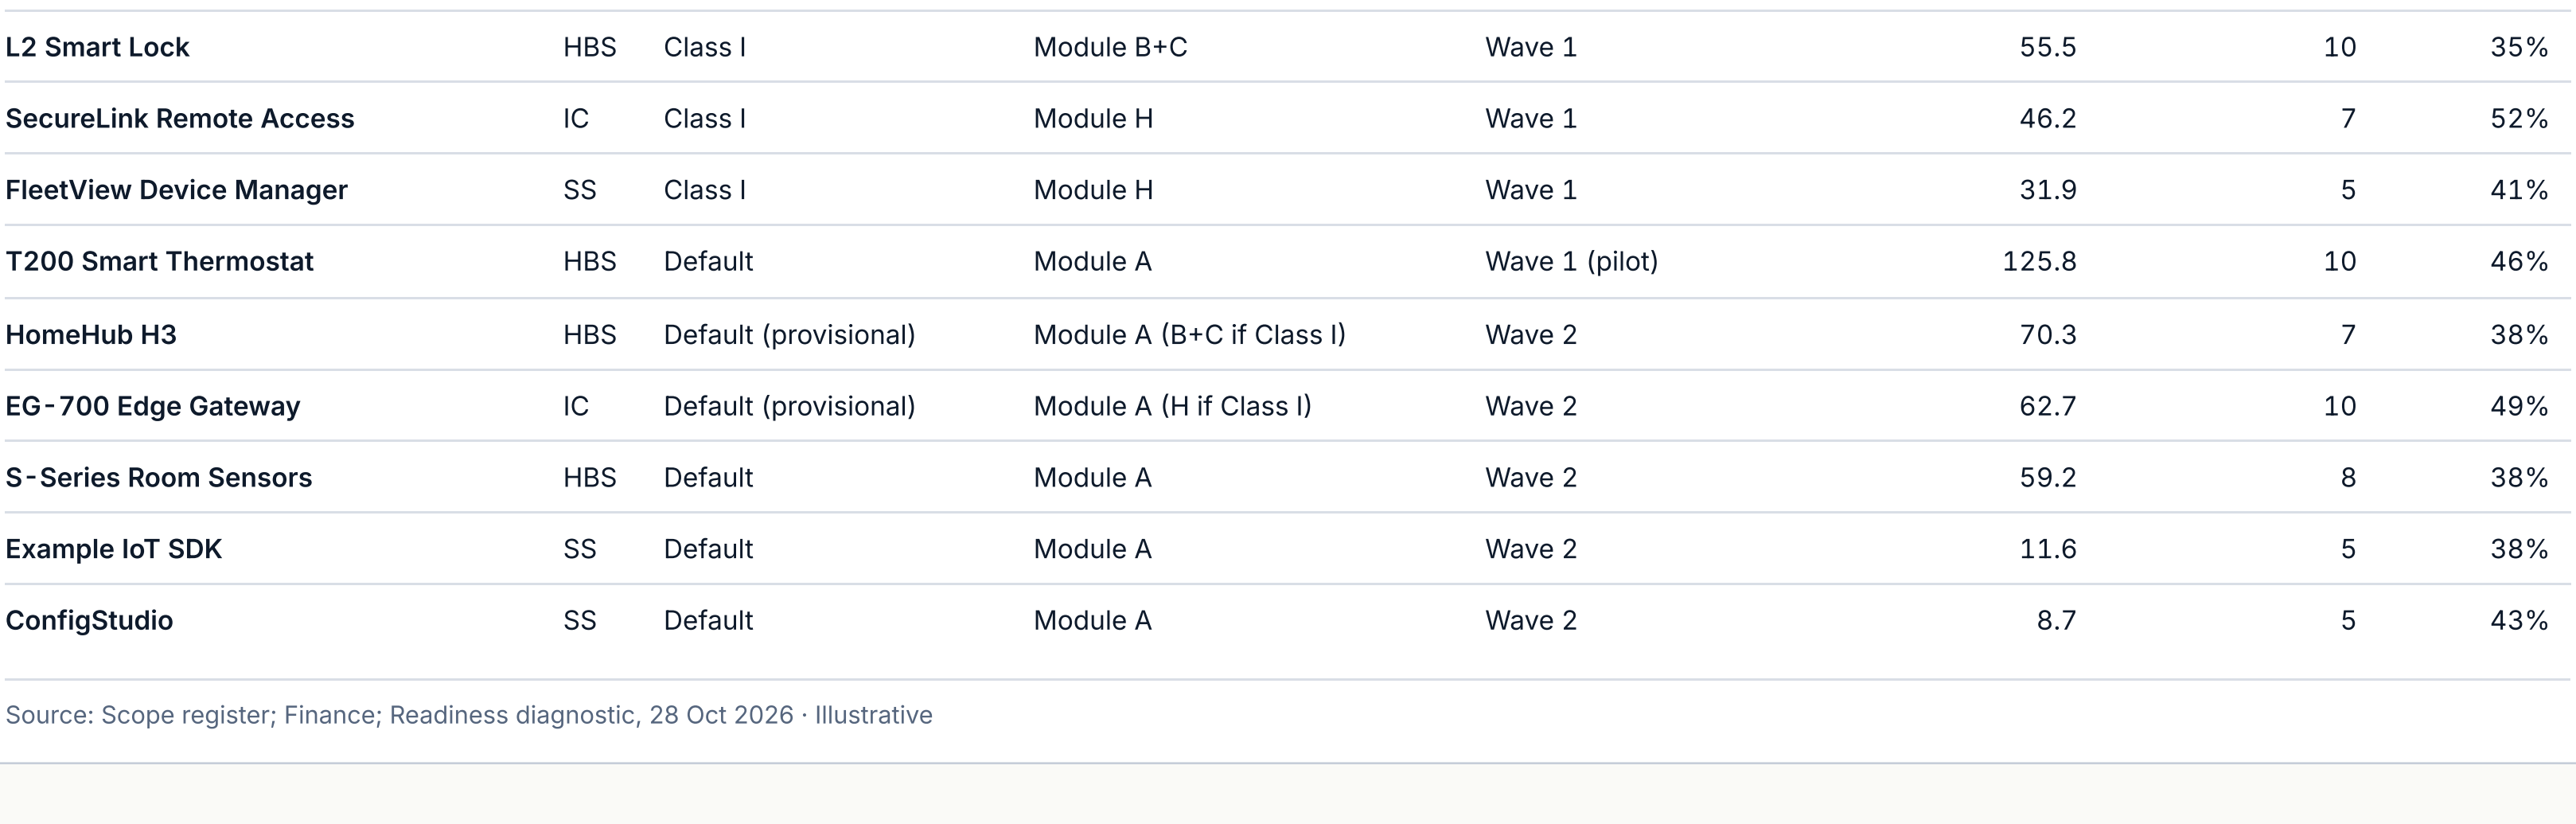

Source: Programme plan (phases, waves and milestones), SteerCo #1 · Illustrative

Workstream status

Lead's assessment reported to SteerCo #1.

ID	Workstream	Lead	RAG	Status note
WS1	**Governance & PMO**	Programme director	● Green	Sponsor named; programme board running; signing instrument drafted for board approval.
WS2	**Portfolio & classification**	Compliance lead	◆ Amber	11 of 13 families classified; EG-700 and HomeHub H3 need legal opinion (borderline Class I).
WS3	**Reporting & PSIRT**	PSIRT lead	● Green	SRP live with 3 Assigned Representatives; first drill filed early warning in 9h 40m.
WS4	**Secure engineering & SDLC**	Product security officer	◆ Amber	T200 pilot risk assessment in review; release gate designed, not yet enforced.
WS5	**SBOM & supply chain**	Head of platform engineering	■ Red	Signed SBOMs on 38% of releases; HBS firmware builds lack binary SCA; 6 of 41 suppliers on CRA clauses.
WS6	**Documentation & evidence**	Compliance lead	◆ Amber	System of record not yet selected; Annex VII outline agreed.
WS7	**Conformity & market access**	Head of quality & regulatory	■ Red	No CRA notified body designated at checks to 8 Sep 2026 (external); 3 candidates shortlisted; V1/L2 route undecided.
WS8	**People & change**	Head of engineering enablement	◆ Amber	140 of 920 engineers trained; works council consultation on PSIRT on-call opened.

Source: Workstream lead reports, SteerCo #1 · Illustrative

Due by 30 Nov 2026

Mobilisation-plan tasks that finish within a month of SteerCo #1, earliest first. The board decision (T02) unlocks the notified-body pre-assessment contracts (T25), due **29 Jan 2027**.

Due	Task	Owner	Status
12 Nov 2026	Board paper and pre-read issued	Programme director	● In progress
19 Nov 2026	Board decisions on budget, signing authority, NB strategy, legacy lines	Executive sponsor	○ Not started
20 Nov 2026	Distribution map per product refreshed for SRP 'Member States' field	Product management	● In progress
27 Nov 2026	Legal opinion on EG-700 and HomeHub H3 classification	General Counsel	● In progress
27 Nov 2026	T200 pilot risk assessment signed (applicability matrix)	Product security officer	● In progress

Source: Mobilisation plan · Illustrative

Milestones

From registration on the Single Reporting Platform to full application of the CRA.

ID	Date	Milestone	Status
M0	10 Sep 2026	SRP registration and coordinator CSIRT decision	● Complete
M1	22 Oct 2026	First Art 14 tabletop drill (actively exploited vulnerability)	● Complete
M2	30 Oct 2026	Programme mobilised; SteerCo #1	● Complete
M3	19 Nov 2026	Board decisions (budget, signing authority, notified-body strategy, legacy lines)	○ Planned
M4	18 Dec 2026	Scope and classification register baselined	● On track
M5	29 Jan 2027	Notified-body pre-assessments contracted (3 candidates)	◆ At risk
M6	26 Feb 2027	Wave 1 risk assessments signed	● On track
M7	31 Mar 2027	Formal notified-body engagements contracted (Module H; Module B+C)	◆ At risk
M8	31 Mar 2027	SBOM pipeline live on all Wave 1 release trains	◆ At risk
M9	16 Apr 2027	Second Art 14 drill (weekend severe-incident scenario)	○ Planned
M10	30 Jun 2027	Update infrastructure hardened (HSM signing, anti-rollback)	○ Planned
M11	30 Sep 2027	Wave 1 technical files complete	○ Planned
M12	30 Nov 2027	Module H approval and Module B certificates	○ Planned
M13	3 Dec 2027	Declarations signed; CE marking; Annex II published	○ Planned
M14	11 Dec 2027	Full application of the CRA	■ Fixed

Source: Programme plan, SteerCo #1 · Illustrative

— MONEY

Spend of EUR 410k is within tolerance of plan; the base case is EUR 9.25m to Dec 2027

The one-off figure includes **15%** contingency; running costs are **EUR 1.84m** a year from 2028. Scenarios range from **EUR 7.93m** to **EUR 11.42m**. Detail is in the Business case and cost model (D10).

ONE-OFF TO DEC 2027

EUR 9.25m

Q4 2026 EUR 1.42m · 2027 EUR 7.83m, contingency included

RUN COST FROM 2028

EUR 1.84m

A year; 0.15% of annual revenue

ONE-OFF AS SHARE OF REVENUE

0.77%

Of one year's revenue (EUR 1.2bn)

ENGINEERING REMEDIATION

26.2 FTE-years

To ring-fence in the 2027 plan (mitigation for R02)

Cumulative spend: plan and actual

EUR, monthly cumulative plan including contingency. The shaded band is the ±10% tolerance around plan.

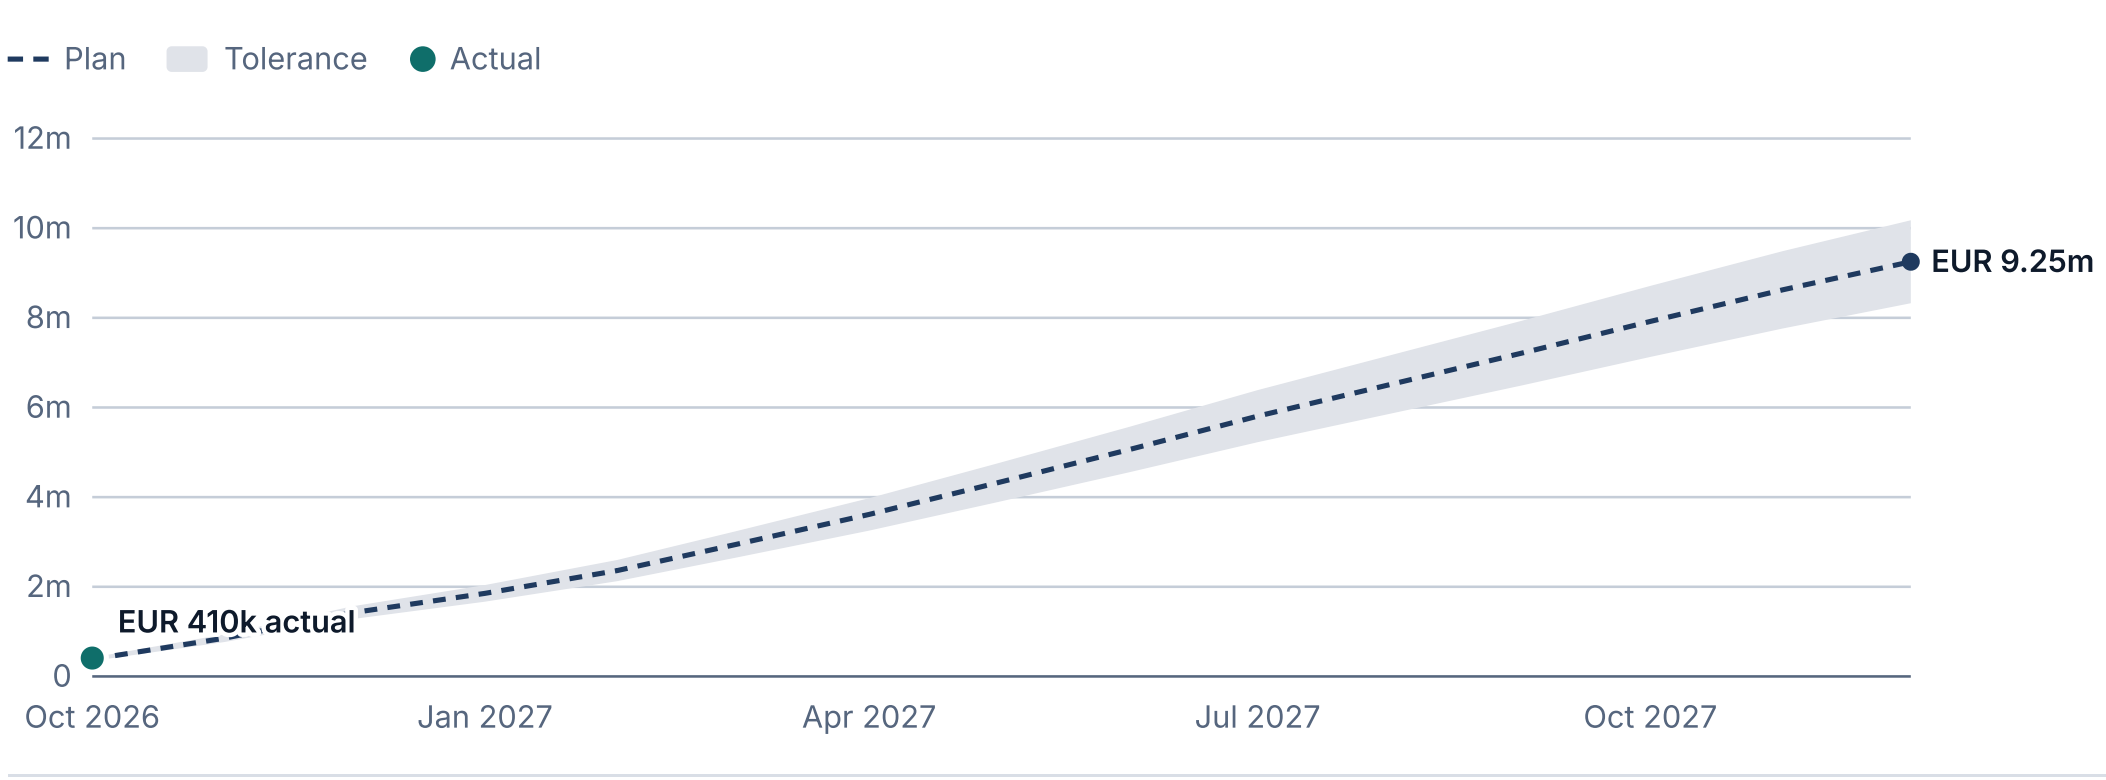

Source: Finance (actual, Oct 2026); Business case and cost model (D10), base case · Illustrative

Spend to date against plan

Cumulative to Oct 2026.

+6.7%

EUR 410k actual against **EUR 384k** plan: +EUR 26k, inside the ±10% tolerance (K11).

Cumulative plan to Nov 2026	**EUR 854k**
Cumulative plan to Dec 2026 (Q4 budget)	**EUR 1.42m**

Source: Finance; cost model monthly plan · Illustrative

One-off budget by workstream

Base case to Dec 2027; contingency shown as its own line. Secure engineering, mostly Annex I remediation, is the largest line at **EUR 4.39m**.

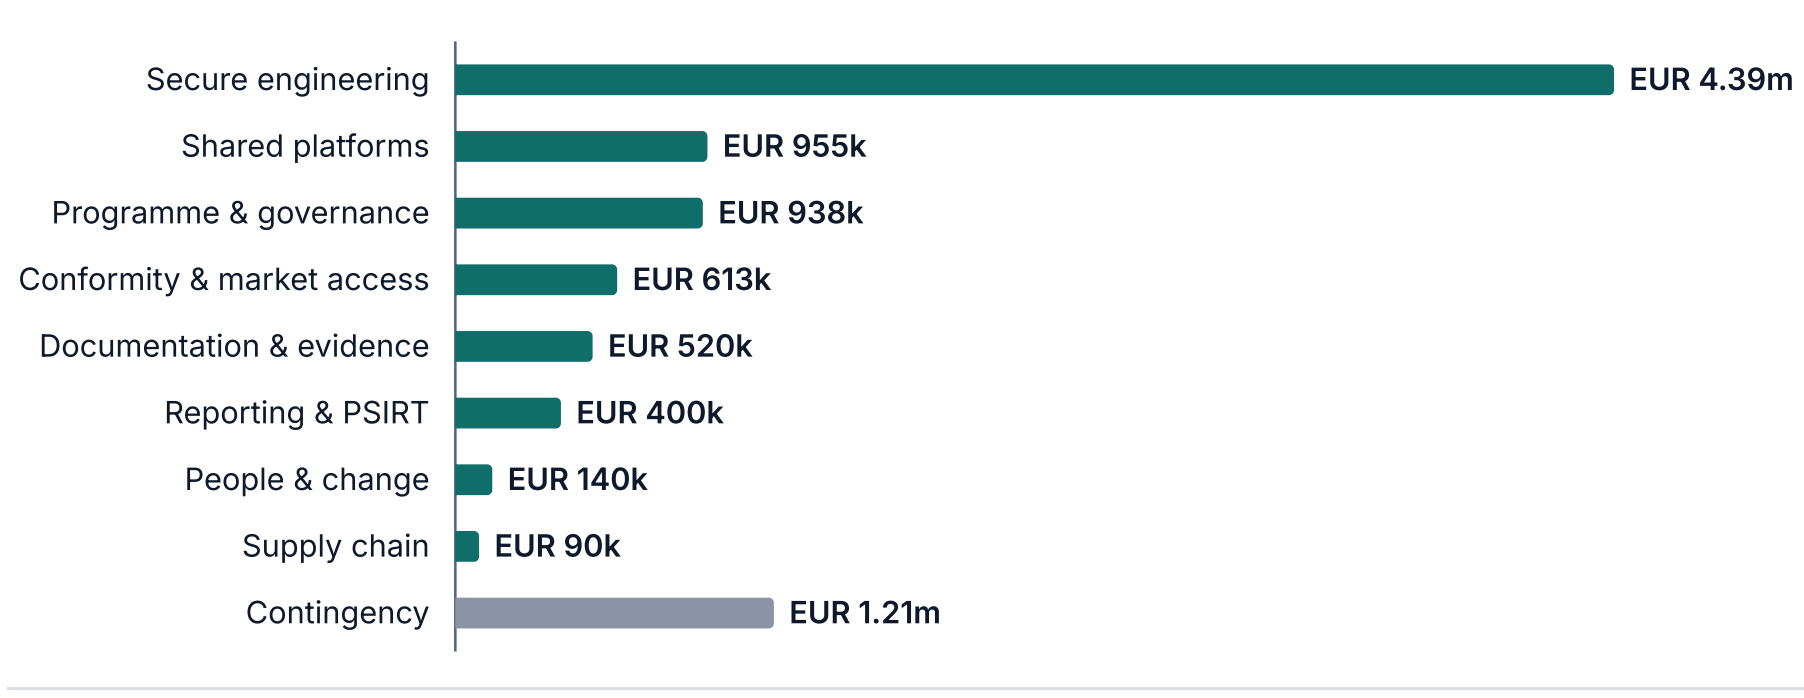

Source: Business case and cost model (D10), base case · Illustrative

Cost scenarios

One-off to Dec 2027 including contingency, and the yearly run cost from 2028.

Scenario	One-off	Run a year	Assumption
Low	EUR 7.93m	EUR 1.76m	Harmonised standards cited mid-2027; less remediation than assessed; fewer notified-body days.
Base	EUR 9.25m	EUR 1.84m	Plan as assessed at the 28 Oct 2026 baseline.
High	EUR 11.42m	EUR 1.90m	Notified-body scarcity forces a second body and premium fees; remediation 30% above estimate; extra programme FTE.

Source: Business case and cost model (D10) · Illustrative

— RISK AND DECISIONS

Notified-body capacity (R01) is the top risk, and it is still rising

R01 scores **20** (likelihood 4, impact 5) and is owned by the Head of quality & regulatory. Engineering capacity (R02) follows at **16**.

Risk matrix: likelihood by impact

Each chip is a risk, marked with its trend: ↑ rising, → stable, ↓ falling, • new. Cell shade shows the rating band.

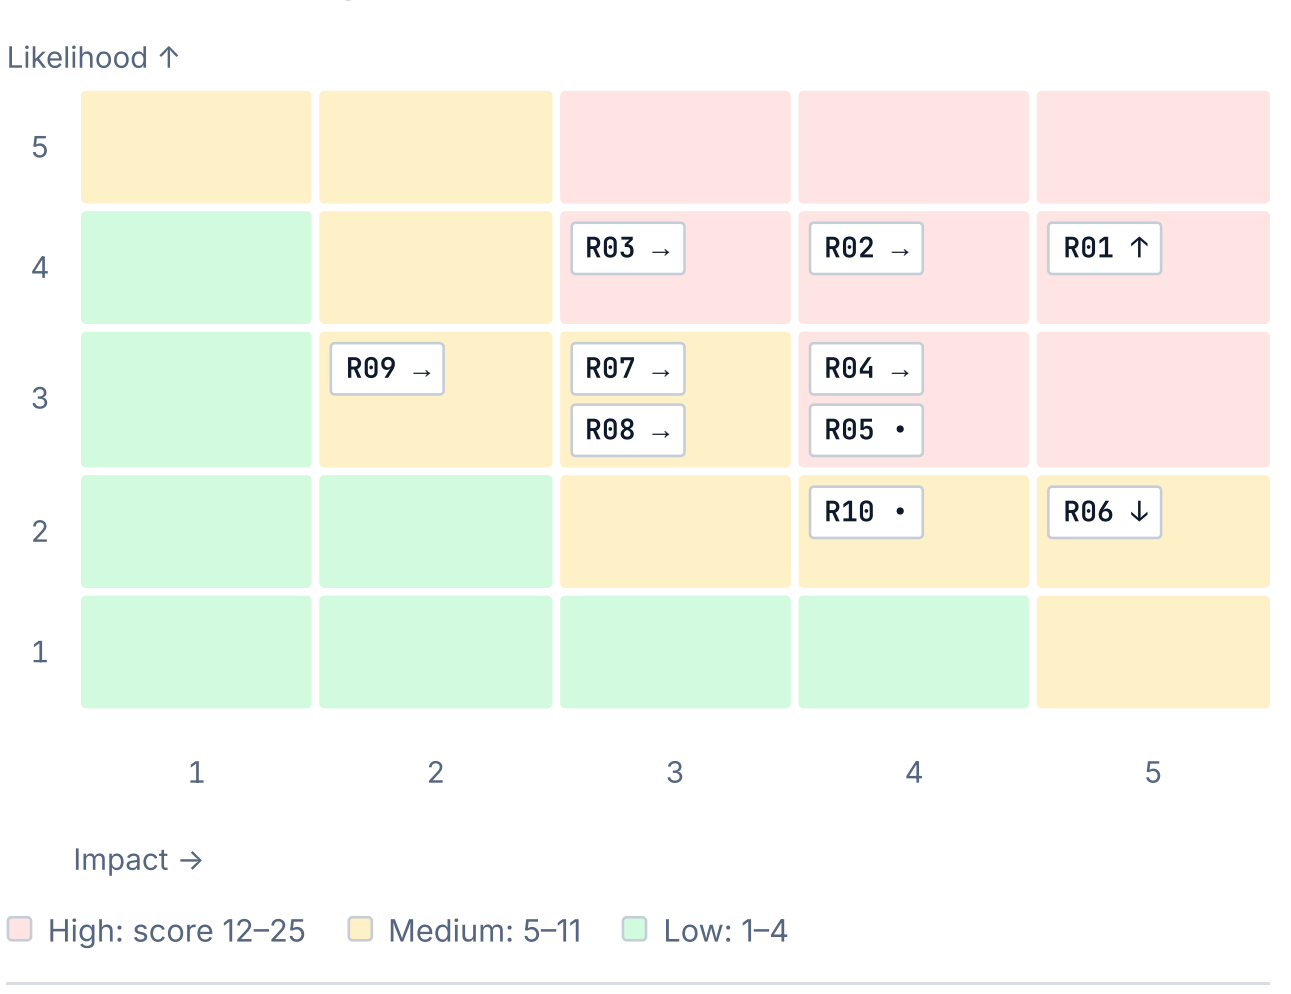

Source: Programme risk register, SteerCo #1 · Illustrative

Top five risks

Ranked by score (likelihood × impact).

ID	Risk	Score	Owner	Mitigation	Trend
R01	**No notified-body capacity in time**	20	Head of quality & regulatory	Pre-contract three candidates with conversion options; Module H for IC to cover five families with one body; check NANDO at every programme board; prioritise top-revenue SKUs.	↑ Rising
R02	**Engineering capacity**	16	CTO	Ring-fence 26 FTE-years in the 2027 plan; defer two roadmap features; contractors for documentation and testing.	→ Stable
R03	**No harmonised standard cited for Class I**	12	Compliance lead	Plan Class I on third-party routes; align files to draft clause structure; switch to Module A only if a citation lands before assessment.	→ Stable
R04	**SBOM and supplier transparency gaps**	12	Head of platform engineering	Binary SCA on firmware images; clause pack to top 15 suppliers first; exit plans for refusers.	→ Stable
R05	**Legacy lines still sold after 11 Dec 2027**	12	BU president IC	Board decision on 19 Nov 2026 to withdraw from EU sale and migrate customers; remediate only if the decision changes.	• New

Source: Programme risk register, SteerCo #1 · Illustrative

Watch list

The remaining risks on the register.

ID	Risk	Score	Owner	Trend
R06	**Late or wrong Art 14 filing**	10	PSIRT lead	↓ Falling
R07	**Scope undercount**	9	Compliance lead	→ Stable
R08	**Key-person dependency in PSIRT**	9	PSIRT lead	→ Stable
R10	**Product-liability disclosure**	8	General Counsel	• New
R09	**Guidance changes**	6	Compliance lead	→ Stable

Source: Programme risk register, SteerCo #1 · Illustrative

Open issues

Problems already affecting delivery, with an owner and a due date.

ID	Issue	Detail	Owner	Due
I01	**Distribution map stale**	The 22 Oct drill showed the 'Member States where available' field could not be completed for two products from current data.	Product management	20 Nov 2026
I02	**Borderline classifications**	EG-700 (cellular uplink routing) and HomeHub H3 (optional alarm mode) could be Class I; notified-body capacity planning includes them until the legal opinion lands.	General Counsel	27 Nov 2026
I03	**HBS firmware SBOM depth**	Manifest-only SBOMs on HBS firmware miss vendored code; binary SCA needed.	Head of platform engineering	15 Jan 2027

Source: Programme issue log, SteerCo #1 · Illustrative

SteerCo #1 decisions, 30 Oct 2026

Recorded outcomes of the first Steering Committee.

ID	Decision	Outcome
SD1	Endorse Module H as the route for Industrial Connectivity and FleetView (five families), using the IEC 62443-4-1 process as the base.	● Endorsed (illustrative)
SD2	Apply the stricter reading to EG-700 and HomeHub H3 until the legal opinion lands on 27 Nov 2026: include them in notified-body capacity planning, keep them in Wave 2 for remediation.	● Endorsed (illustrative)
SD3	Release EUR 0.75m of pre-approval spend ahead of the 19 Nov board.	● Endorsed (illustrative)
SD4	Approve system-of-record selection criteria.	● Endorsed (illustrative)

Source: SteerCo #1 decision log · Illustrative

Board asks, 19 Nov 2026

Decisions the board is asked to take; see the board briefing deck (D01).

ID	Ask	Detail
BD1	**Approve the Project Rampart investment envelope.**	EUR 9.3m one-off to Dec 2027 (incl. 15% contingency) and EUR 1.8m a year run from 2028.
BD2	**Appoint the accountable executive and execute the DoC signing instrument.**	CTO as accountable executive; CEO signs declarations or delegates in writing; compliance lead counter-signs the pre-signature checklist.
BD3	**Authorise notified-body pre-contracting.**	Pre-assessments with three candidate bodies (up to EUR 60k) and formal contracts by Q1 2027 (Module H for IC + FleetView; Module B+C for V1 and L2).
BD4	**Adopt the product-risk acceptance rule.**	Cost, risk appetite and commercial strategy are not grounds to leave product risk unaddressed (guidance paras 156-163); appeals go to the executive sponsor.
BD5	**Withdraw IR-300 and IS-200 from EU sale before 11 Dec 2027.**	EUR 18m of declining EU revenue versus about EUR 1.4m remediation plus notified-body fees; migrate customers to IR-500 and IS-300.

Source: Board paper for 19 Nov 2026 · Illustrative

Client data as at 30 Oct 2026 (SteerCo #1). Regulatory facts verified to 30 Oct 2026, except the notified-body count, which reflects NANDO and Single Market Compliance Space checks to 8 Sep 2026. Illustrative engagement: Example Group is fictional and its figures are illustrative; replace them with the client's data.

Related deliverables: Business case and cost model (D10); Obligations register and programme tracker (D11); CRA Readiness Diagnostic (D08).

Prepared by [Advisor] · Project Rampart · Illustrative · 31 Oct 2026
