ADVISORY

PROJECT RAMPART · MONTHLY MANAGEMENT UPDATE

# Project Rampart — Steering Committee #1

Status as at 30 Oct 2026. Programme Amber: four decisions today and five escalations to the board on 19 Nov 2026

AGENDA

# Four decisions today; the rest of this pack reports by exception


01 **Status on a page**
Programme Amber: reporting on track, market access at risk · p3

02 **Performance**
KPIs 5 Green, 6 Amber, 1 Red; readiness baseline 44% · p4–5

03 **Delivery**
Milestones, Art 14 reporting, market access and budget · p6–9

04 **Risks and issues**
Five High risks, led by notified-body capacity (R01) · p10

05 **Decisions and next 30 days**
SD1–SD4 today; BD1–BD5 for the board on 19 Nov 2026 · p11–12


## DECISIONS SOUGHT TODAY

- SD1 Endorse Module H for Industrial Connectivity and FleetView (five families)
- SD2 Plan notified-body capacity for EG-700 and HomeHub H3 until the legal opinion on 27 Nov
- SD3 Release EUR 0.75m of spend ahead of board approval on 19 Nov
- SD4 Approve the system-of-record selection criteria

Then confirm BD1–BD5 for the board on 19 Nov 2026 (p11)

# Amber: reporting works; market access waits on notified bodies

**Programme: Amber** **Reporting capability on track; market access at risk because no CRA notified body was designated at checks to 8 Sep 2026 (external dependency)**

| | | | |
|---|---|---|---|
| WS1 | **Governance & PMO** | Green | Sponsor named; programme board running; signing instrument drafted for board approval |
| WS2 | **Portfolio & classification** | Amber | 11 of 13 families classified; EG-700 and HomeHub H3 borderline Class I, opinion due 27 Nov |
| WS3 | **Reporting & PSIRT** | Green | SRP live with 3 Assigned Representatives; first drill filed early warning in 9h 40m |
| WS4 | **Secure engineering & SDLC** | Amber | T200 pilot risk assessment in review; release gate designed, not yet enforced |
| WS5 | **SBOM & supply chain** | Red | Signed SBOMs on 38% of releases; HBS firmware lacks binary SCA; 6 / 41 suppliers on clauses |
| WS6 | **Documentation & evidence** | Amber | System of record not yet selected; Annex VII outline agreed |
| WS7 | **Conformity & market access** | Red | No CRA notified body designated at checks to 8 Sep 2026 (external); 3 candidates shortlisted; V1/L2 route undecided |
| WS8 | **People & change** | Amber | 140 of 920 engineers trained; works council consultation on PSIRT on-call opened |

## THREE WINS

**SRP registered:** 3 Assigned Representatives; CSIRT decided (M0)

**First drill:** early warning in 9h 40m against 24 hours (M1)

**Baseline:** all 13 families diagnosed; readiness index 44%

## THREE CONCERNS

**No notified body designated:** EUR 468m of EU revenue needs one

**SBOM coverage 38%:** target 100% of releases by 31 Mar 2027

**V1/L2 route undecided:** 5 of 7 Class I/II families have a plan

Source: workstream reports and KPI register, as at 30 Oct 2026; readiness diagnostic, 28 Oct 2026; Illustrative

# Reporting KPIs are Green; signed SBOMs at 38% are the only Red


Twelve programme KPIs as at 30 Oct 2026: 5 Green, 6 Amber, 1 Red

| ID | KPI | Value | Target | RAG | Trend | Source |
|---|---|---|---|---|---|---|
| K01 | Portfolio readiness index | 44% | 70% Jun 2027; 90% Nov 2027 | Amber | Baseline | Diagnostic |
| K02 | Scope and class decided | 11 / 13 | 13 / 13 by 18 Dec 2026 | Amber | New | Scope register |
| K03 | Class I/II route and NB plan | 5 / 7 | 7 / 7 by 19 Nov 2026 | Amber | New | Scope register |
| K04 | SRP Assigned Representatives | 3 | ≥ 2 at all times | Green | Stable | SRP roster |
| K05 | Drill: time to early warning | 9h 40m | < 24h incl. weekends | Green | First drill | Drill record |
| K06 | Art 14 cases (reportable / not) | 0 / 4 | 100% decided, UTC timeline | Green | Stable | PSIRT case files |
| K07 | **Signed SBOMs, last 30 days** | **38% (9 / 24)** | 100% by 31 Mar 2027 | Red | Up from 21% | Build pipeline |
| K08 | Signed risk assessments | 0 / 13 (T200 in review) | Wave 1 (8) by 26 Feb 2027 | Green | On plan | System of record |
| K09 | Suppliers on CRA clauses | 6 / 41 (15%) | Top 15 Jan 2027; all Jun 2027 | Amber | New | Contract register |
| K10 | Engineers trained | 140 / 920 (15%) | 60% by Mar 2027 | Amber | Up | LMS |
| K11 | Spend to date vs plan | EUR 0.41m vs EUR 0.38m | Within ±10% of plan | Green | Oct 2026 | Finance |
| K12 | Notified-body candidates | 3 shortlisted; 1 proposal | 3 pre-assessments contracted by 29 Jan 2027 | Amber | New | Programme |


Source: KPI owners' systems as listed; diagnostic baseline 28 Oct 2026; drill record 22 Oct 2026; Illustrative

# Readiness is 44%: evidence and market access lag most, and Class I home products trail

By domain, % of target

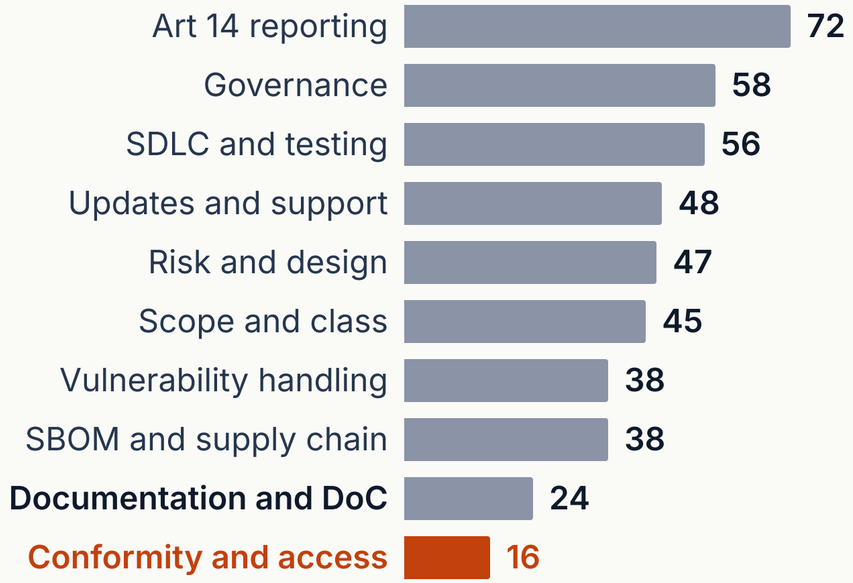


By family, % of target

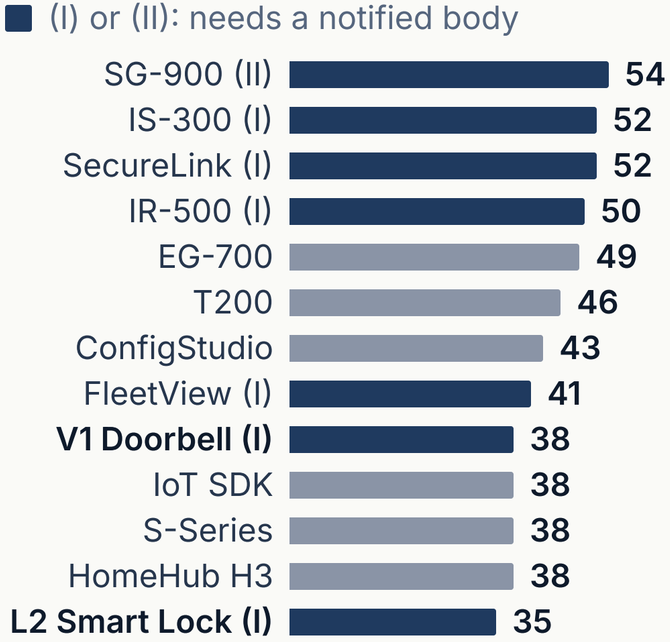


**44%**

Portfolio readiness index, 28 Oct 2026. Target 70% by Jun 2027 and 90% by Nov 2027

## WHAT THIS MEANS

**Reporting leads at 72%,** short of the 100% Art 14 needs now

**Evidence lags:** documentation 24%, conformity and access 16%

**Class I home products trail:** L2 35% and V1 38%, both in Wave 1


Source: CRA Readiness Diagnostic (D08), 13 families, baseline 28 Oct 2026; target = level 3 on every question; Illustrative

# M0–M2 are complete; M5, M7 and M8 are At risk on notified bodies and SBOMs

| ID | Date | Milestone | Status |
|---|---|---|---|
| M0 | 10 Sep 2026 | SRP registration and coordinator CSIRT decision | Complete |
| M1 | 22 Oct 2026 | First Art 14 tabletop drill | Complete |
| M2 | 30 Oct 2026 | Programme mobilised; SteerCo #1 | Complete |
| M3 | 19 Nov 2026 | Board decisions (BD1–BD5) | Planned |
| M4 | 18 Dec 2026 | Scope and classification register baselined | On track |
| M5 | 29 Jan 2027 | Notified-body pre-assessments contracted (3)<br>No CRA body designated at 8 Sep 2026 checks; BD3 pre-contracting | At risk |
| M6 | 26 Feb 2027 | Wave 1 risk assessments signed | On track |
| M7 | 31 Mar 2027 | Formal notified-body engagements (H; B+C)<br>Depends on first designations (external) | At risk |
| M8 | 31 Mar 2027 | SBOM pipeline live on all Wave 1 release trains<br>Needs binary SCA on HBS firmware first (I03) | At risk |

Source: Obligations register and programme tracker (D11), as at 30 Oct 2026; Illustrative

Phases, Sep 2026 to Dec 2027

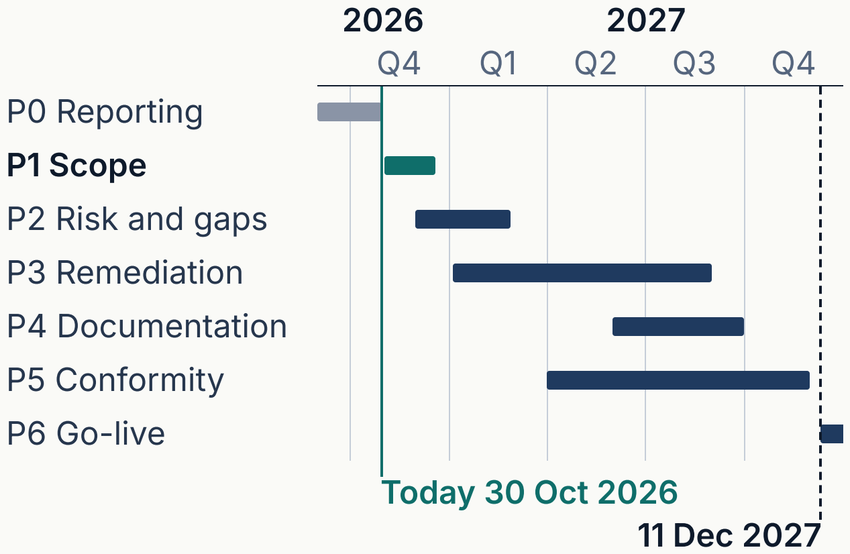



Grey complete · teal current · navy planned

# Reporting works: the first drill filed an early warning in 9h 40m, inside 24 hours

Drill 1, 22 Oct 2026: actively exploited vulnerability (tabletop), hours from awareness

**Before the clock:** first signal triaged against written awareness criteria




## IN PLACE

**SRP:** 3 Assigned Representatives registered (at least 2 required)

**Coordinator CSIRT:** Germany, the main establishment (M0)

**Cases:** 4 assessed, 0 reportable, all with UTC decision records

## OPEN ITEMS

**I01 stale distribution map:** SRP field fix (T10) due 20 Nov 2026

**T14 legacy inventory:** T100, H2 and V0 fleets, due 11 Dec 2026

**T11 works council:** 24/7 on-call agreement, due 18 Dec 2026

## NEXT

**M9, 16 Apr 2027:** second drill, weekend severe-incident scenario


**Incident clocks:** 24h, 72h, then a final report one month after notification

**R06 late or wrong filing:** rated Medium, trend falling

Source: drill record, 22 Oct 2026; SRP roster; PSIRT case files; risk register; CRA Art 14(2) and (4); Illustrative

# EUR 468m of EU revenue needs a notified body; none as at 8 Sep 2026

EU revenue of the 13 in-scope families by conformity route, EUR m (EUR 806.6m in total)




## NOTIFIED BODIES, AS AT 30 OCT 2026

**None designated:** no CRA body in NANDO at checks to 8 Sep 2026

**Art 35(2):** Member States to strive for enough bodies by 11 Dec 2026

**Pipeline:** 3 candidates shortlisted; 1 proposal received

**At risk:** M5 pre-assessments 29 Jan 2027; M7 contracts 31 Mar 2027

## STANDARDS WATCH, AS AT 30 OCT 2026

**No harmonised standard cited:** Class I cannot use Module A

**EN 40000-1-1/-1-2:** ratification 2 Nov 2026, not for citation

**prEN 40000-1-3:** HAS assessment submitted 3 Aug 2026; outcome not public


**ETSI EN 304 6xx:** enquiries close mid-Sep to mid-Nov 2026

**DECISIONS** SD1 (Module H) and SD2 (stricter reading) today; BD3 notified-body pre-contracting at the 19 Nov board

Source: Example Group revenue by family; Commission NANDO checks to 8 Sep 2026; standards dates per secondary trackers; Illustrative

# Spend is EUR 410k against a EUR 384k plan (+7%), within tolerance

Cumulative spend, EUR m, Oct 2026 to Dec 2027; plan includes 15% contingency

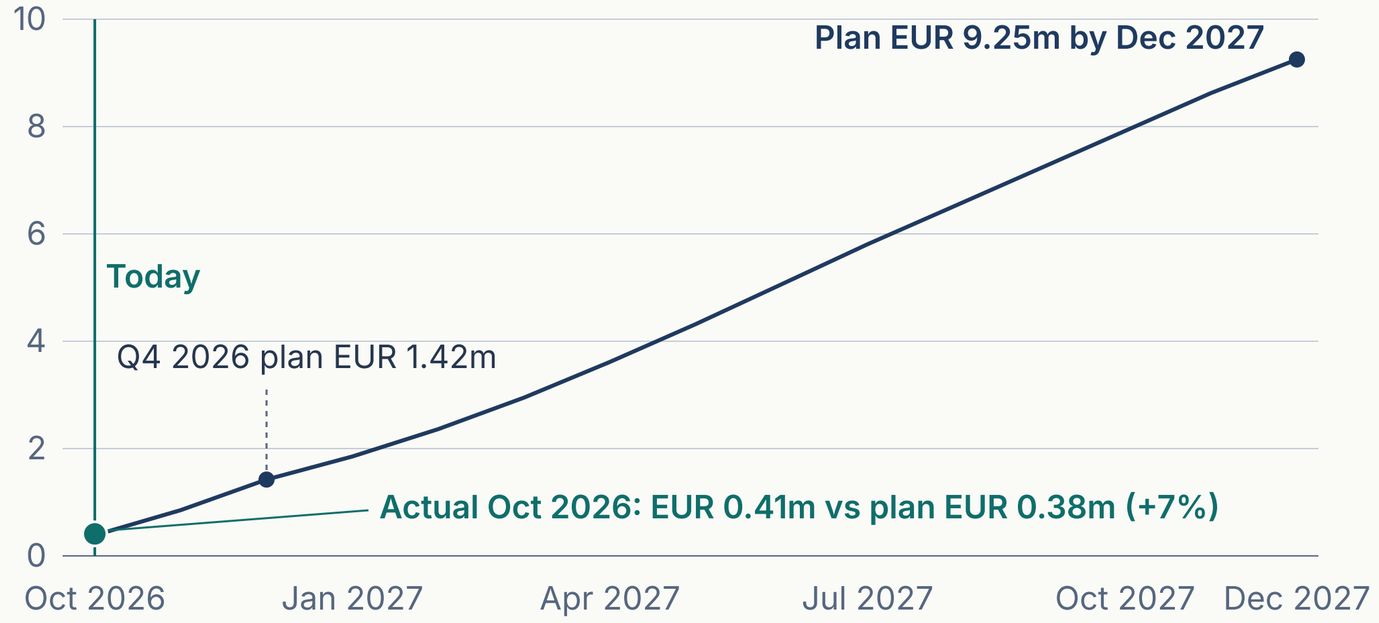


## BASE PLAN TO DEC 2027

| | |
|---|---|
| Q4 2026, incl. contingency | EUR 1.42m |
| 2027, incl. contingency | EUR 7.83m |
| **One-off to Dec 2027** | **EUR 9.25m** |
| Run from 2028, a year | EUR 1.84m |

## ASKS

**SD3 today:** release EUR 0.75m of spend ahead of board approval


**BD1 on 19 Nov:** EUR 9.3m one-off, incl. 15% contingency, and EUR 1.8m a year to run

**Range:** EUR 7.9m low to EUR 11.4m high (scenarios in D10)

Source: Finance actuals, Oct 2026; Business case and cost model (D10), base-case monthly plan; Illustrative

# Five risks are High; notified-body capacity (R01, score 20) is rising

Likelihood ↑ by impact →, all ten risks

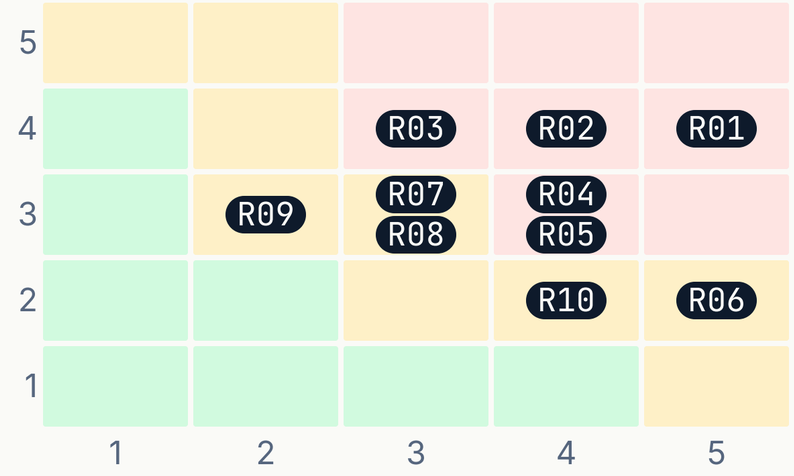


| ID | Top five risks and mitigation | Owner | Trend |
|---|---|---|---|
| R01<br>**20** | **No notified-body capacity in time**<br>Pre-contract 3 candidates; Module H for 5 families | Head of quality & regulatory | **Rising** |
| R02<br>**16** | **Engineering capacity**<br>Ring-fence 26 FTE-years in 2027; defer two features | CTO | Stable |
| R03<br>**12** | **No harmonised standard cited for Class I**<br>Plan Class I on third-party routes until a citation | Compliance lead | Stable |
| R04<br>**12** | **SBOM and supplier transparency gaps**<br>Binary SCA on firmware; clauses to top 15 suppliers | Head of platform engineering | Stable |
| R05<br>**12** | **Legacy lines still sold after 11 Dec 2027**<br>Withdraw IR-300 and IS-200 from EU sale (BD5) | BU president IC | New |

## OPEN ISSUES

**I01 · Distribution map stale**
Product management
Due 20 Nov 2026

**I02 · Borderline classifications**
General Counsel
Due 27 Nov 2026

**I03 · HBS firmware SBOM depth**
Head of platform engineering
Due 15 Jan 2027

Source: Risk and issue register (D11), as at 30 Oct 2026; score = likelihood × impact; High 12–25, Medium 5–11, Low 1–4; Illustrative

# Decide SD1–SD4 today; take BD1–BD5 to the board on 19 Nov 2026

## TODAY · STEERCO #1, 30 OCT 2026

| | | |
|---|---|---|
| SD1 | **Endorse Module H as the route for Industrial Connectivity and FleetView (five families), on the IEC 62443-4-1 process** | Recommendation: endorse · Outcome: Endorsed (illustrative) |
| SD2 | **Apply the stricter reading to EG-700 and HomeHub H3 until the 27 Nov opinion: plan body capacity, keep them in Wave 2** | Recommendation: endorse · Outcome: Endorsed (illustrative) |
| SD3 | **Release EUR 0.75m of pre-approval spend before the board** | Recommendation: endorse · Outcome: Endorsed (illustrative) |
| SD4 | **Approve the system-of-record selection criteria** | Recommendation: endorse · Outcome: Endorsed (illustrative) |

## TO THE BOARD · 19 NOV 2026

| | | |
|---|---|---|
| BD1 | **Approve the Project Rampart investment envelope** | EUR 9.3m one-off, incl. 15% contingency; EUR 1.8m a year run |
| BD2 | **Appoint the accountable executive and execute the DoC signing instrument** | CTO accountable; CEO signs or delegates in writing |
| BD3 | **Authorise notified-body pre-contracting** | Three pre-assessments up to EUR 60k; contracts by Q1 2027 |
| BD4 | **Adopt the product-risk acceptance rule** | Cost, risk appetite and commercial strategy are no grounds to leave risk open |
| BD5 | **Withdraw IR-300 and IS-200 from EU sale before 11 Dec 2027** | EUR 18m of declining EU revenue; remediation about EUR 1.4m |

Source: SteerCo #1 decision log, 30 Oct 2026; board paper for 19 Nov 2026; outcomes recorded after the meeting; Illustrative

# Five tasks fall due by 30 Nov 2026; the 12 Nov board paper gates the critical path

Due by 30 Nov 2026, from the mobilisation plan (T01–T30)

| ID | Task | Owner | Due | Status |
|---|---|---|---|---|
| T01 | **Board paper and pre-read issued** | Programme director | 12 Nov | In progress |
| T02 | Board decisions on BD1–BD5 | Executive sponsor | 19 Nov | Not started |
| T10 | Distribution map refreshed for SRP | Product management | 20 Nov | In progress |
| T07 | EG-700 and H3 legal opinion | General Counsel | 27 Nov | In progress |
| T15 | T200 pilot risk assessment signed | Product security officer | 27 Nov | In progress |

### CRITICAL PATH

**T01 board paper (12 Nov)** → **T02 board decisions (19 Nov)** → then T03 DoC signing instrument (4 Dec), T27 withdraw-or-remediate plan for IR-300 and IS-200 (18 Dec) and T25 notified-body pre-assessment contracts (29 Jan 2027)

### STARTING BY 30 NOV 2026

| | | |
|---|---|---|
| T08 | Remote-function maps (13) | 9 Nov |
| T13 | security.txt and CVD policy | 9 Nov |
| T19 | Dependency-Track and EUVD | 9 Nov |
| T16 | Release gate, T200 and IR-500 | 16 Nov |
| T20 | Clause pack, top 15 suppliers | 16 Nov |
| T23 | Annex II template, T200 first | 16 Nov |
| T26 | Module H scope statement | 16 Nov |
| T29 | Sales briefing, customer FAQ | 16 Nov |
| T03 | DoC signing instrument | 20 Nov |
| T27 | Withdraw-or-remediate plan | 20 Nov |
| T21 | Supplier questionnaire to 41 | 23 Nov |
| T30 | Staff awareness pulse survey | 23 Nov |
| T17 | Wave 1 threat models | 30 Nov |

Source: Mobilisation plan T01–T30, Obligations register and programme tracker (D11), as at 30 Oct 2026; Illustrative

# WS1 and WS3 are Green; WS2 and WS4 await legal and CTO calls

| Workstream and lead | Objective | Progress this month | Next steps | Help needed |
|---|---|---|---|---|
| WS1 Green<br>**Governance & PMO**<br>Programme director | Decision rights, funding and monthly governance | Sponsor named; programme board running; signing instrument drafted | T01 board paper 12 Nov; T04 risk rule 11 Dec; T05 system of record 18 Dec | SD3 and SD4 today |
| WS2 Amber<br>**Portfolio & classification**<br>Compliance lead | Every product has a class, a route and an owner | 11 of 13 families classified; EG-700 and H3 borderline Class I | T07 legal opinion 27 Nov; T06 inventories 4 Dec; T08 maps 11 Dec; T09 register 18 Dec | SD2 today; legal opinion by 27 Nov |
| WS3 Green<br>**Reporting & PSIRT**<br>PSIRT lead | Every Art 14 report on time, 24/7, legacy included | SRP live; drill 9h 40m; 4 cases assessed, none reportable | T10 map 20 Nov; T14 legacy inventory 11 Dec; T11 works council 18 Dec; T12 hire 29 Jan | HR to close the 24/7 on-call agreement |
| WS4 Amber<br>**Secure engineering & SDLC**<br>Product security officer | Annex I met per family via an enforced gate | T200 pilot risk assessment in review; gate designed, not enforced | T15 T200 sign-off 27 Nov; T16 gate on T200 and IR-500 22 Jan; T17 threat models 26 Feb | CTO to ring-fence 26 FTE-years in the 2027 plan (R02) |

Source: workstream reports; mobilisation plan in the programme tracker (D11), as at 30 Oct 2026; Illustrative

# WS5 and WS7 are Red; both need decisions above the workstream

| Workstream and lead | Objective | Progress this month | Next steps | Help needed |
|---|---|---|---|---|
| WS5 Red<br>**SBOM & supply chain**<br>Head of platform engineering | Signed SBOM per release; suppliers on CRA clauses | Signed SBOMs 38%; HBS firmware lacks binary SCA; 6 of 41 suppliers on clauses | T19 and T21 by 18 Dec; T18 binary SCA 15 Jan; T20 clause pack 29 Jan | Procurement to back exit plans for refusing suppliers (R04) |
| WS6 Amber<br>**Documentation & evidence**<br>Compliance lead | Versioned Annex VII and Annex II per family | Annex VII outline agreed; system of record not yet selected | T22 Annex VII template 4 Dec; T23 Annex II template and T05 system of record 18 Dec | SD4: approve the selection criteria today |
| WS7 Red<br>**Conformity & market access**<br>Head of quality & regulatory | Certificate or internal-control record per family | No CRA body designated at 8 Sep 2026 checks; 3 shortlisted, 1 proposal; V1/L2 route open | T24 proposals 11 Dec; T27 legacy plan 18 Dec; T26 Module H scope 22 Jan; T25 contracts 29 Jan | SD1 today; BD3 and BD5 on 19 Nov |
| WS8 Amber<br>**People & change**<br>Head of engineering enablement | Engineers, sales and support know their CRA duties | 140 of 920 engineers trained (15%); on-call consultation opened | T30 pulse survey 4 Dec; T29 sales briefing and FAQ 11 Dec; T28 400 engineers 29 Jan | BU presidents to release engineers for training |

Source: workstream reports; mobilisation plan in the programme tracker (D11), as at 30 Oct 2026; Illustrative

# Each number has one source and one owner; refresh the pack five working days before SteerCo

Where each number comes from, and who refreshes it

| System of record | Feeds | Owner |
|---|---|---|
| CRA Readiness Diagnostic (D08) | K01 · p5 | Compliance lead |
| Scope register | K02, K03 · p8 | Compliance lead |
| SRP roster; drill records; case files | K04–K06 · p7 | PSIRT lead |
| Build pipeline | K07 | Head of platform engineering |
| System of record (evidence) | K08 | Product security officer |
| Contract register | K09 | Head of procurement |
| LMS | K10 | Head of engineering enablement |
| Finance ledger; cost model (D10) | K11 · p9 | CFO delegate |
| Notified-body tracker; NANDO check | K12 · p8 | Head of quality & regulatory |
| Programme tracker; risk register (D11) | p3, p6, p10–12 | PMO |

## MONTHLY CYCLE (WORKING DAYS)

- T-5 Owners refresh their systems
- T-4 PMO updates tables and charts
- T-3 Leads confirm RAG and notes
- T-2 Sponsor review; decisions drafted
- T-1 Pre-read issued to the committee

## RAG RULES

**Green:** on plan; no help needed from SteerCo

**Amber:** off plan, but the workstream lead can recover it within the phase

**Red:** off plan and not recoverable without a SteerCo decision or an external fix

Note: template defaults; D08, D10 and D11 are the pack’s readiness diagnostic, cost model and programme tracker
