PROJECT RAMPART · BOARD BRIEFING · PRE-READ

Keeping our EU market open: the Cyber Resilience Act

What the regulation requires of Example Group, what readiness costs and the five decisions we ask of the board

Illustrative engagement: fictional client data; regulatory facts verified to 30 Oct 2026

EXECUTIVE SUMMARY

We keep selling in the EU after 11 Dec 2027 if we act within two quarters

THE CASE IN FOUR LINES

Situation. The CRA makes cybersecurity a condition of CE marking. Reporting applies now; everything else from 11 Dec 2027.

Complication. Seven of 13 families, EUR 468m of EU revenue, need a notified body or a cited standard. Neither exists yet.

Question. What must we do, by when and at what cost, to keep selling in the EU after 11 Dec 2027?

Answer. Project Rampart: build shared capabilities once, apply them per product and book notified-body capacity by Q1 2027.

THREE MESSAGES

1. **Reporting is already law**
   Every in-scope product, legacy included, is on a 24-hour clock today.

2. **Market access is the binding constraint**
   EUR 468m of EU revenue needs a notified body that does not yet exist.

3. **Compliance is an evidence system**
   Build once, prove it per product version for ten years; we start at 44% readiness.

DECISION REQUIRED Five decisions today, including **EUR 9.3m** to Dec 2027 and EUR 1.8m a year to run

Source: CRA Arts 14, 32, 71; readiness diagnostic, 28 Oct 2026; Project Rampart business case; Illustrative

DECISIONS REQUESTED

Five decisions today keep our 11 Dec 2027 deadline achievable

ID	DECISION	WHY NOW	IF WE WAIT
BD1	**Approve the investment envelope:** EUR 9.3m to Dec 2027 incl. 15% contingency; EUR 1.8m a year from 2028	26.2 FTE-years must be ring-fenced in the 2027 plan	Remediation competes with the 2027 roadmap; Wave 1 slips
BD2	**Appoint the CTO as accountable executive** and execute the DoC signing instrument	Release gates are enforced from Jan 2027	No one can block a release or sign a declaration
BD3	**Authorise notified-body pre-contracting:** three pre-assessments (up to EUR 60k); contracts by Q1 2027	Pre-assessments due 29 Jan 2027; slots are scarce	**EUR 468m** of EU revenue has no assessment slot
BD4	**Adopt the product-risk acceptance rule:** cost, risk appetite and commercial strategy are no grounds to leave risk open	Wave 1 risk assessments are signed by 26 Feb 2027	Risk decisions that would not survive market surveillance
BD5	**Withdraw IR-300 and IS-200 from EU sale** before 11 Dec 2027; migrate customers to IR-500 and IS-300	Customers need lead time; the plan is due 18 Dec 2026	EUR 1.4m plus fees to keep EUR 18m of declining revenue

Detail: investment on slide 16; notified-body critical path on slide 8; decision rights on slide 15; legacy lines on slide 17

Source: Project Rampart board paper; integrated plan (M5, M6, T16, T27); business case; Illustrative

The CRA puts cybersecurity under CE marking for every product we sell

Hardware + **Firmware and software** + **Companion apps** + **Backends we build** = **One product with digital elements**

01
Secure by design
A risk assessment per product; no known exploitable vulnerabilities at release

Art 13; Annex I Part I

02
Vulnerability handling
SBOM, disclosure policy and security updates through the support period

Annex I Part II; Art 13(8)

03
Reporting
Exploited vulnerabilities and severe incidents reported via ENISA within 24 hours

Art 14; live since 11 Sep 2026

04
Evidence and conformity
Technical file, assessment, declaration and CE marking; kept at least 10 years


Arts 13(13), 28–32

Who carries the duties. Almost all fall on us as manufacturer (Arts 13–14). Importers and distributors must check CE marking, declarations and documentation (Arts 19–20). Backends a product needs for a function count as part of it (Art 3(2)).

Source: Regulation (EU) 2024/2847 Arts 2–3, 13–14, 19–20, 28–32, Annexes I and VII; knowledge base, as at 30 Oct 2026

Reporting is already live; everything else applies in 387 days

CRA application dates; scale linear from Jun 2026, compressed before

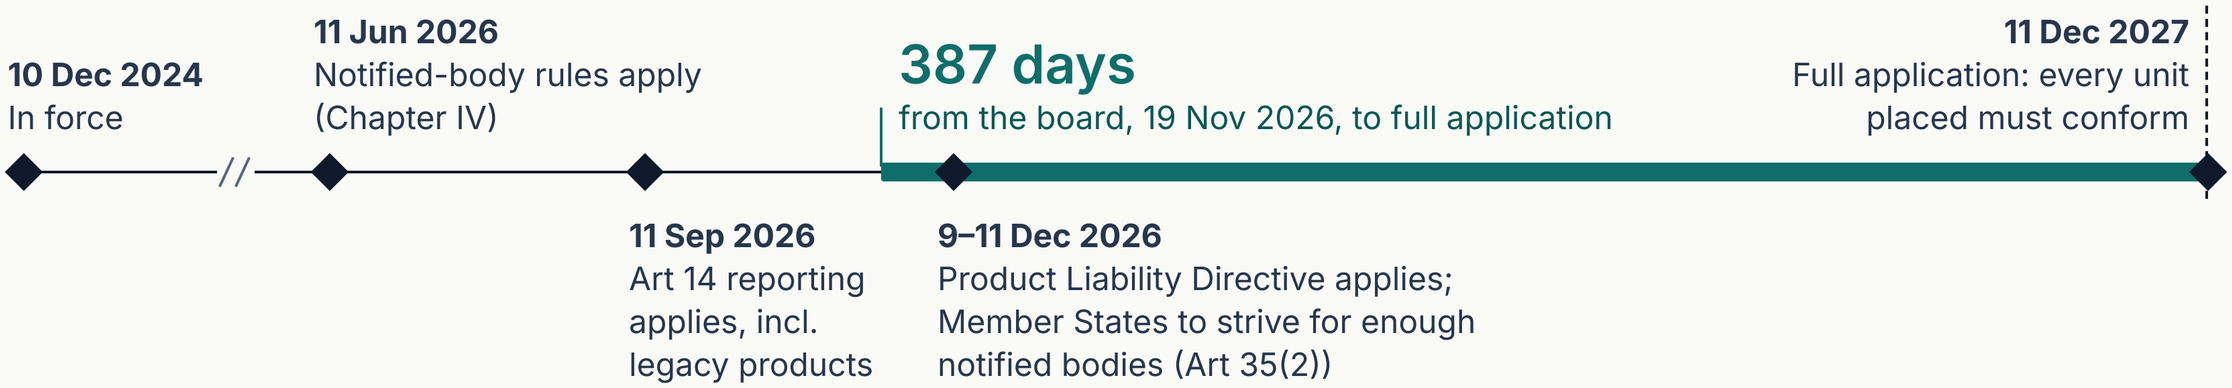

Per-unit rule. Reporting already covers every product we have placed on the market (Art 69(3)); the full requirements bind each unit placed from 11 Dec 2027 (Art 69(2)).

Source: Regulation (EU) 2024/2847 Arts 35(2), 69, 71; Directive (EU) 2024/2853 Art 2; facts as at 30 Oct 2026

Thirteen families and EUR 807m of EU revenue fall inside the CRA

Needs a notified body: EUR 468.3m, 58% of in-scope EU revenue


EU revenue, EUR m	**Default** · 6 families Self-assessment (Module A)		**Class I** · 6 families Third-party route today		**Class II** · 1 family Always third-party		**Total**
Home & Building Solutions	T200 Thermostat S-Series Sensors HomeHub H3*	125.8 59.2 70.3	V1 Doorbell L2 Smart Lock	74.0 55.5	–		**384.8**
Industrial Connectivity	EG-700 Gateway*	62.7	IR-500 Router IS-300 Switch SecureLink	108.9 79.2 46.2	SG-900 Firewall/IDS	72.6	**369.6**
Software & Services	ConfigStudio IoT SDK	8.7 11.6	FleetView	31.9	–		**52.2**
Total, 13 families		**338.3**		**395.7**		**72.6**	806.6

* Borderline Class I; opinion due 27 Nov 2026. Excludes EUR 17.4m EU SaaS revenue (group EU total EUR 824m) and 7 legacy lines.

Source: Example Group product register and finance, EU revenue (EUR m); Implementing Regulation (EU) 2025/2392; Illustrative

Seven families, EUR 468m of EU revenue, cannot be self-certified today

EU revenue by CRA class, EUR m, 13 product families

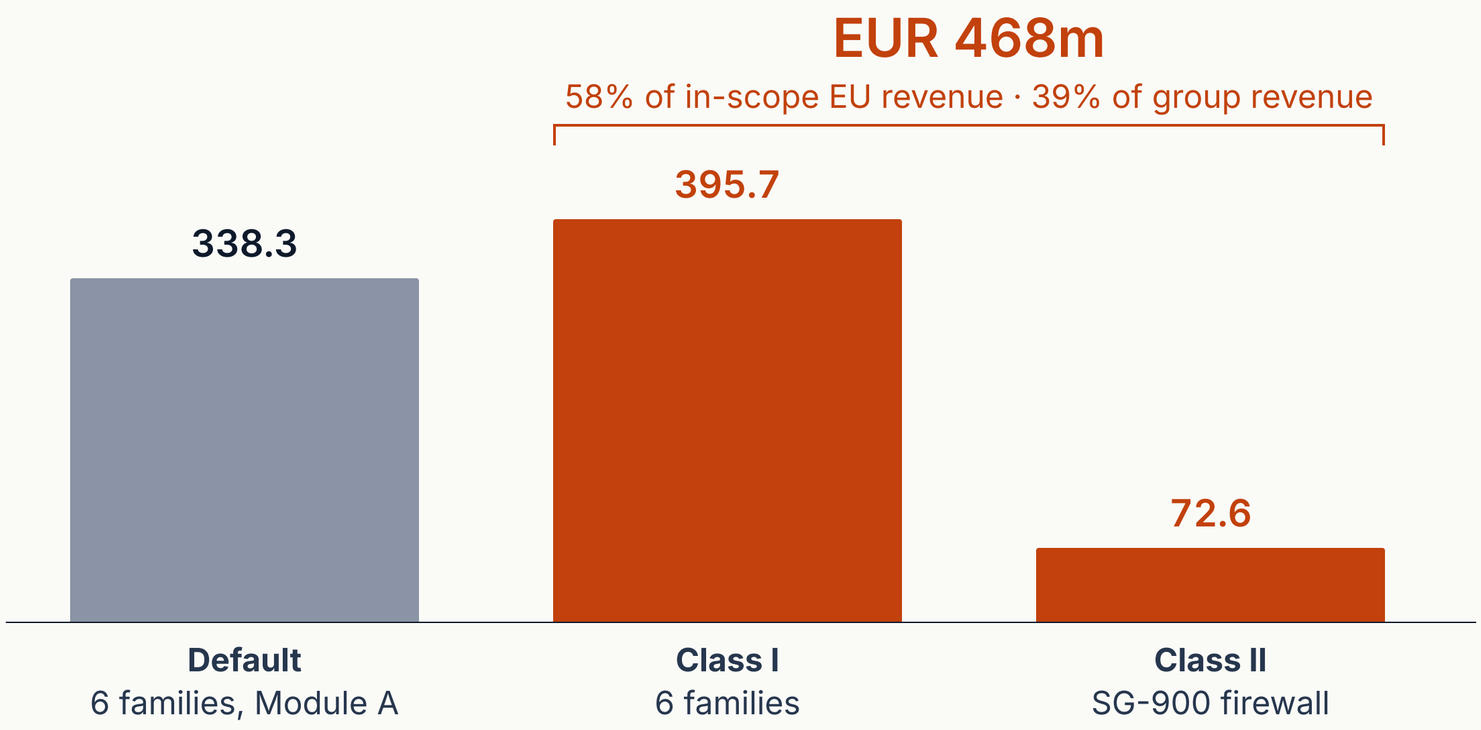

WHY NO ROUTE EXISTS TODAY

Class I may self-assess only by fully applying a harmonised standard cited in the Official Journal. None is cited.

Class II needs a notified body; no EU-certificate route exists yet, and no body was verifiably designated.

If H3 and EG-700 are ruled Class I, exposure rises to EUR 601m; the legal opinion is due 27 Nov 2026.

Source: Example Group finance (illustrative); CRA Art 32; Commission, as at 30 Oct 2026; NANDO checks to 8 Sep 2026; Illustrative

Notified-body capacity, not engineering, sets our critical path




Our routes: Module H for five IC and S&S families with one body; Module B+C for the V1 doorbell and L2 lock.

Lead times are commentary, unverified: 12–18 months to designate a body; 2–4 months to contract; 3–6 months per Module B+C engagement.

Source: Project Rampart integrated plan (M5, M7, M11, M12); CRA Decoded (commentary, unverified); vendor statements; Illustrative

Fines cap at EUR 30m, but market access puts EUR 468m a year at risk

Annual EU revenue that needs a notified body versus maximum fines for Example Group, EUR m

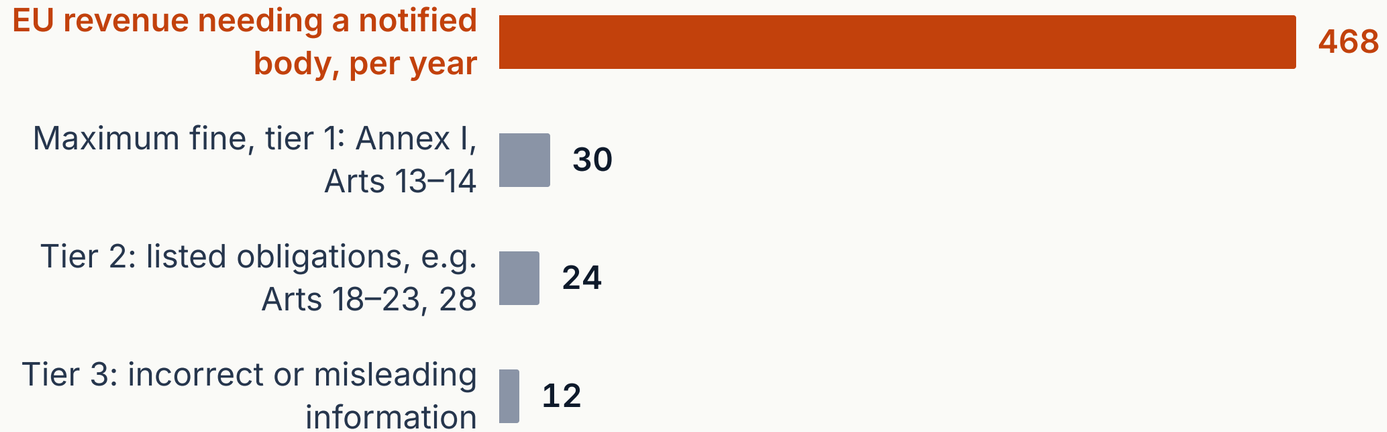

BEYOND FINES

Withdrawal or recall can be ordered, and one national finding can extend EU-wide (Arts 54–58).

Product liability from 9 Dec 2026: a vulnerability can be a defect, and our files can be disclosed.


Customers under NIS2 and DORA will ask for our declaration, SBOM and support period.

Each fine is the higher of EUR 15m, 10m or 5m and 2.5%, 2% or 1% of worldwide turnover; at EUR 1.2bn the percentage applies. Fines apply from 11 Dec 2027.

Source: CRA Art 64(2)–(4), Arts 54–58; Directive (EU) 2024/2853 Arts 9–10; Example Group revenue EUR 1.2bn; Illustrative

The market is late: only 29% of German firms know what the CRA means for them

Selected 2026 surveys, % of respondents; each labelled with its source, base and type

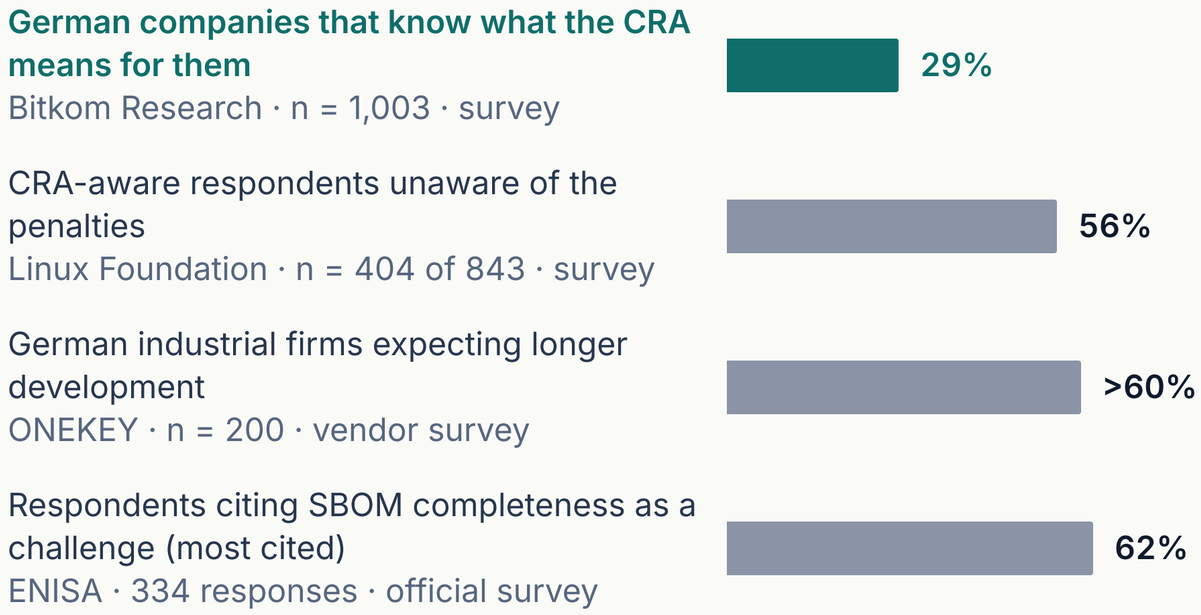

0

CRA notified bodies verifiably designated at the last check, 8 Sep 2026 (official and vendor sources)

SO WHAT

Move before the market does. When demand peaks in 2027, assessment slots and product-security specialists will be scarce.

Sources: Bitkom Research (Apr–Jun 2026); Linux Foundation Research (2026); ONEKEY (Sep 2026); ENISA (Jun 2026); Commission

We start at 44% readiness, weakest where market access is decided

Level 0–4	Governance	Scope & class	Risk & design	SDLC & testing	SBOM & supply chain	Vulnerability handling	Updates & support	Art 14 reporting	Documentation & DoC	Conformity & access	Index
T200 Thermostat	1.75	1.50	2.00	1.00	1.25	0.50	1.75	2.00	1.00	1.00	46%
S-Series Sensors	1.75	1.00	1.25	1.00	0.50	0.75	2.00	2.00	0.50	0.50	38%
HomeHub H3	1.75	0.75	1.25	1.00	0.50	1.00	1.75	2.00	0.75	0.50	38%
V1 Doorbell	1.75	1.25	1.50	1.00	1.00	0.50	1.75	2.00	0.50	0.25	**38%**
L2 Smart Lock	1.75	1.00	1.25	1.00	0.50	0.75	1.50	2.00	0.50	0.25	**35%**
IR-500 Router	1.75	1.50	1.50	2.50	1.00	1.75	1.75	2.25	0.75	0.25	50%
IS-300 Switch	1.75	1.75	1.50	2.50	1.25	1.75	1.50	2.25	1.00	0.50	52%
EG-700 Gateway	1.75	1.50	1.75	2.00	1.00	1.75	1.75	2.25	0.50	0.50	49%
SG-900 Firewall	1.75	1.25	2.00	2.50	1.25	2.00	1.25	2.25	1.00	1.00	54%
SecureLink	1.75	1.50	1.50	2.25	1.50	1.75	1.75	2.25	0.75	0.75	52%
FleetView	1.75	1.75	1.00	1.75	1.25	0.75	1.00	2.25	0.50	0.25	41%
ConfigStudio	1.75	1.75	1.00	1.75	1.75	1.00	0.50	2.25	1.00	0.25	43%
IoT SDK	1.75	1.00	0.75	1.50	2.00	0.75	0.50	2.25	0.75	0.25	38%
Portfolio average	1.75	1.35	1.40	1.67	1.13	1.15	1.44	2.15	0.73	0.48	44%

Domain index: reporting 72%, documentation 24%, conformity 16%. **Least ready:** L2 Smart Lock 35%, V1 Doorbell 38%, both Class I.

Colour = level reached, rounded down: red 0 Not started · orange 1 Initial · yellow 2 Defined · green 3 Implemented, the target · teal 4 Assured

Source: CRA Readiness Diagnostic, 40 questions, self-assessed and moderated, 28 Oct 2026; index = mean of min(level, 3) / 3; Illustrative

Reporting works today: our first drill filed an early warning in 9h 40m

0h
Awareness
The clock starts once we are reasonably certain

→

24h
Early warning
Filed on ENISA's platform; our drill took 9h 40m

→

72h
Notification
Details, measures taken and advice for users

→

14 days
Final report
After a fix; incidents: 1 month after submitting the 72h notification

WORKING TODAY

3 Assigned Representatives on ENISA's platform (target 2 or more)

Germany recorded as coordinator CSIRT, 10 Sep 2026

4 cases assessed since 11 Sep 2026; none reportable

9h 40m to early warning in the drill of 22 Oct 2026

GAPS TO CLOSE

Distribution map stale for 2 products: fix by 20 Nov 2026

Legacy fleet, incl. 1.1m T100 units: inventory by 11 Dec 2026

24/7 on-call: works council agreement by 18 Dec 2026

PSIRT key-person risk: PSIRT lead hired by 29 Jan 2027

Source: CRA Art 14(2), (4); drill record, 22 Oct 2026; SRP roster; PSIRT case files; integrated plan (T10–T14); Illustrative

Project Rampart builds shared capabilities once and applies them product by product

BUILT ONCE · FIVE SHARED CAPABILITIES

- PSIRT and reporting
- SBOM and supply chain
- Secure update infrastructure
- Evidence system of record
- Policies and training

↓ feed every product family


APPLIED PER FAMILY · 13 FAMILIES IN WAVES 1 AND 2; THE T200 PILOT SETS THE TEMPLATES

Scope and class → Risk assessment → Remediation → Technical file → **Conformity assessment** → Declaration and CE marking

GOVERNED BY The CTO as accountable executive · a monthly programme board · named decision rights

Source: Project Rampart programme design; conformity assessment is the step gated by notified-body capacity; Illustrative

A 14-month, three-wave plan has every family declared by 3 Dec 2027

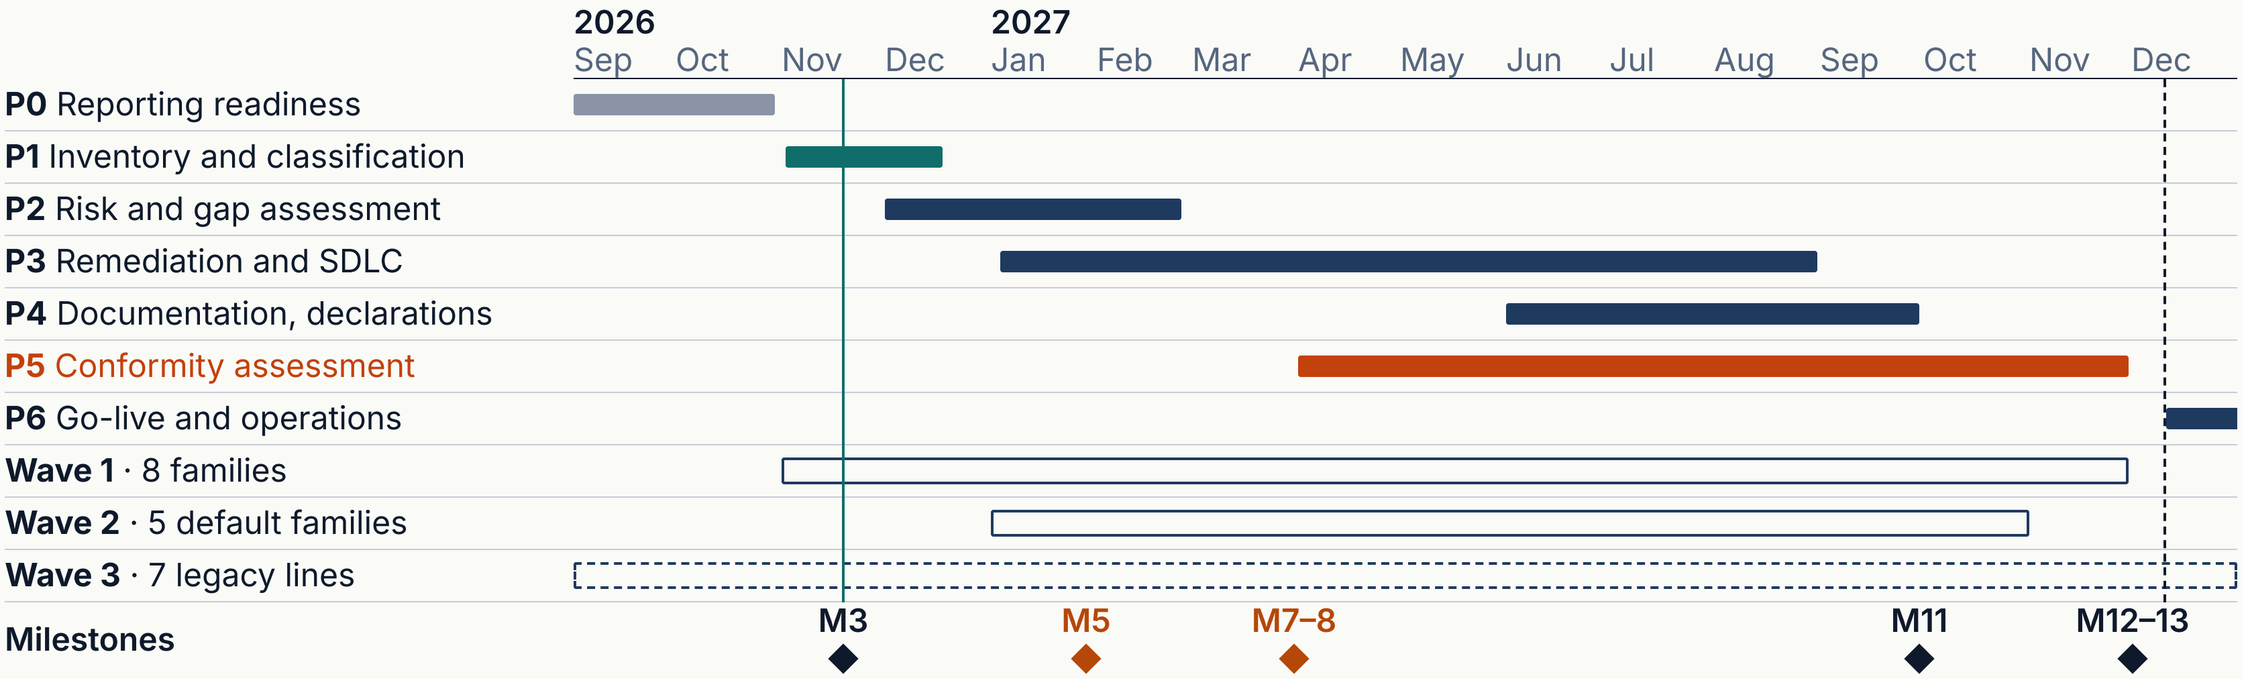

M3 board, 19 Nov (teal line) · **M5** pre-assessments, 29 Jan, at risk · **M7–8** notified-body contracts and SBOM pipeline, 31 Mar, at risk · **M11** Wave 1 files, 30 Sep · **M12–13** certificates and declarations, 30 Nov–3 Dec · dashed line: 11 Dec 2027

Source: Project Rampart integrated plan and milestone register, 30 Oct 2026; P0 complete (grey), P1 in progress (teal); Illustrative

Three decisions cannot wait for a committee, so each has a named holder

REPORTING CLOCK

Declaring awareness of an exploited vulnerability

Holder: PSIRT lead, 24/7, with two named deputies

Rule: no approval before the 24-hour early warning; legal reviews the 72-hour and final reports

Art 14; guidance para 213

PRODUCT RISK

Accepting residual product risk

Holder: product security officer; appeal to the executive sponsor

Rule: cost, risk appetite and commercial strategy are not valid reasons to leave risk unaddressed

Guidance paras 156–163; board decision BD4

DECLARATION OF CONFORMITY

Signing the EU declaration of conformity

Holder: CEO, or a delegate named in writing

Rule: signs only on a pre-signature checklist counter-signed by the compliance lead


Art 28; board decision BD2

FORUMS PSIRT review weekly · programme board monthly · standards and guidance review quarterly · executive review quarterly

Source: Project Rampart governance design; CRA Arts 14, 28; guidance C(2026) 5252 (approved draft, non-binding); Illustrative

Readiness costs EUR 9.3m to Dec 2027, 0.77% of one year's revenue

One-off cost to Dec 2027 by workstream, base case, EUR k

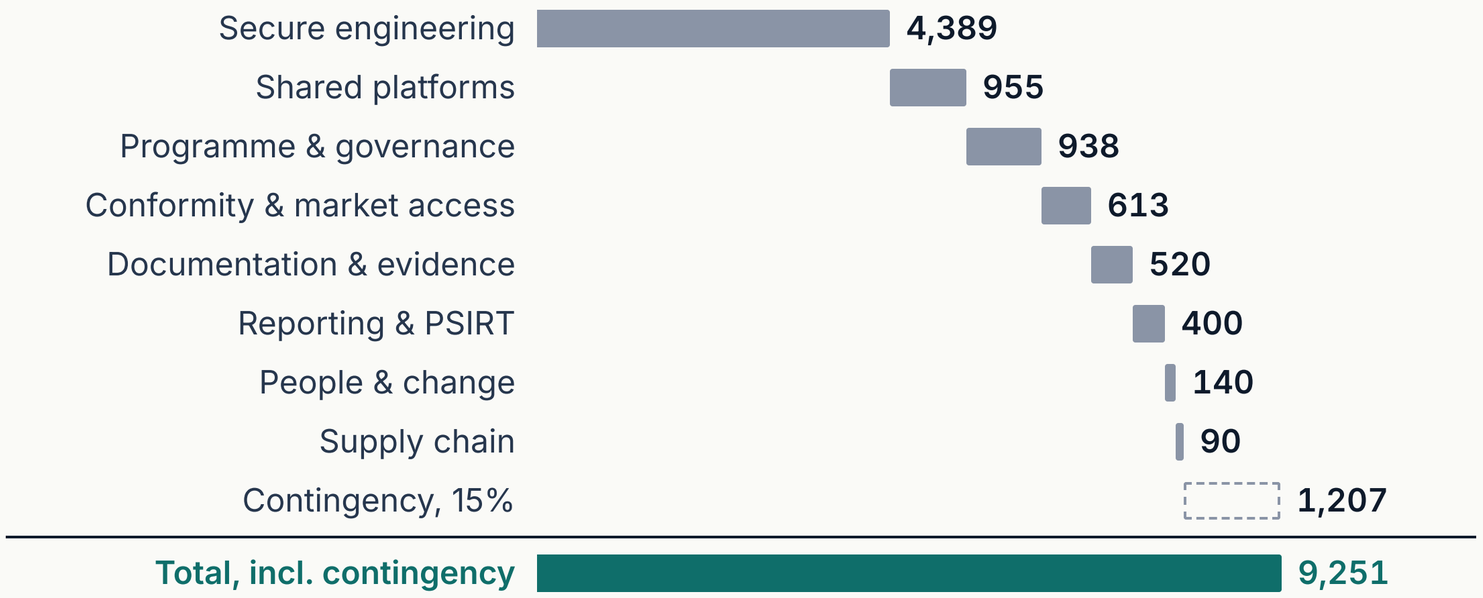

Rounded to EUR k, so items may not sum exactly; total EUR 9,251,175

IN CONTEXT

EUR 1.8m a year
to run from 2028 (EUR 1.76m–1.90m across scenarios)

EUR 7.9m–11.4m
one-off range; low if standards are cited mid-2027, high if a second body is needed

EUR 1.4m + EUR 7.8m
phasing: Q4 2026, then 2027, incl. contingency

EUR 468m · EUR 30m
annual EU revenue it protects · maximum fine, tier 1

Source: Project Rampart business case, base case, real 2026 EUR excl. VAT; one-off to Dec 2027; Illustrative


Withdrawing two declining legacy lines from EU sale avoids EUR 1.4m of remediation

	OPTION A **Remediate and keep selling**	OPTION B · RECOMMENDED (BD5) **Withdraw from EU sale and migrate**
COST	About EUR 1.4m plus notified-body fees, and two more products in the assessment queue	No remediation or fees; notified-body capacity stays on IR-500 and IS-300
REVENUE	Keeps EUR 18m of declining EU revenue: IR-300 EUR 11m, IS-200 EUR 7m	Customers move to IR-500 and IS-300; the withdrawal plan is due 18 Dec 2026
REPORTING	Art 14 reporting continues for the 235k units in the field	Unchanged: reporting for the installed base continues either way

Why now: any unit placed on the EU market after 11 Dec 2027 must comply, however old its design (Art 69(2)).

Source: Example Group finance and installed base (IR-300 95k, IS-200 140k units); remediation estimate; CRA Art 69(2)–(3); Illustrative

Five high risks could stop us; each has an owner and a mitigation

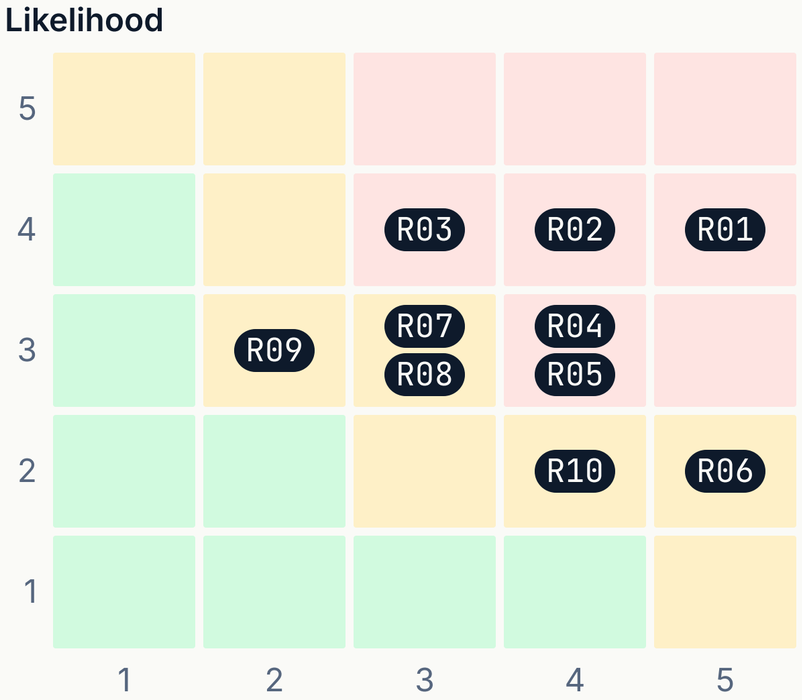

HIGH RISKS · OWNER · MITIGATION

R01 No notified-body capacity in time · rising · Head of quality & regulatory
Pre-contract three bodies; one Module H body covers five families

R02 Engineering capacity · CTO
Ring-fence 26 FTE-years in the 2027 plan; defer two roadmap features

R03 No harmonised standard cited for Class I · Compliance lead
Plan Class I on third-party routes; use Module A only if a standard is cited

R04 SBOM and supplier gaps · Head of platform engineering
Binary analysis of firmware; CRA clauses to the top 15 suppliers first

R05 Legacy lines sold after 11 Dec 2027 · BU president IC
Withdraw IR-300 and IS-200 from EU sale and migrate customers (BD5)

Medium: R06 late Art 14 filing (falling) · R07 scope undercount · R08 PSIRT key people · R09 guidance changes · R10 liability disclosure

Source: Project Rampart risk register, 30 Oct 2026; score = likelihood × impact, each 1–5; Illustrative

In the next 90 days we move from decision to contracted capacity

NOVEMBER 2026

Decide

19 Nov · Board decisions BD1–BD5 (M3)

20 Nov · Distribution map refreshed for reporting

27 Nov · Legal opinion on EG-700 and HomeHub H3

27 Nov · T200 pilot risk assessment signed

DECEMBER 2026

Baseline

4 Dec · DoC signing instrument executed

11 Dec · Product-risk rule added to the risk framework; proposals from three candidate bodies

18 Dec · Scope and classification register baselined (M4)

18 Dec · System of record chosen; on-call agreed with the works council; legacy withdrawal plan

JANUARY 2027

Contract

15 Jan · SBOMs generated from HBS firmware binaries

22 Jan · Release gate enforced on T200 and IR-500

29 Jan · Pre-assessments contracted with three bodies (M5, at risk)

29 Jan · CRA clauses issued to the top 15 suppliers; PSIRT lead hired

Source: Project Rampart mobilisation plan (T01–T30) and milestones M3–M5, 30 Oct 2026; Illustrative

Seven families need third-party assessment; two await a legal opinion

Family	BU	Class (Annex III item)	EU revenue, EUR m	Route	Wave	Support, years	Readiness
T200 Thermostat	HBS	Default	125.8	Module A	1 (pilot)	10	46%
S-Series Sensors	HBS	Default	59.2	Module A	2	8	38%
HomeHub H3	HBS	Default; review vs Class I item 17	70.3	A; B+C if Class I	2	7	38%
V1 Doorbell	HBS	Class I, item 17 (cameras)	74.0	Module B+C	1	7	38%
L2 Smart Lock	HBS	Class I, item 17 (smart locks)	55.5	Module B+C	1	10	35%
IR-500 Router	IC	Class I, item 12 (routers)	108.9	Module H	1	12	50%
IS-300 Switch	IC	Class I, item 12 (switches)	79.2	Module H	1	12	52%
EG-700 Gateway	IC	Default; review vs Class I item 12	62.7	A; H if Class I	2	10	49%
SG-900 Firewall/IDS	IC	Class II, item 2 (firewalls, IDS)	72.6	Module H	1	10	54%
SecureLink	IC	Class I, item 5 (VPN)	46.2	Module H	1	7	52%
FleetView	S&S	Class I, item 6 (network management)	31.9	Module H	1	5	41%
ConfigStudio	S&S	Default	8.7	Module A	2	5	43%
IoT SDK	S&S	Default	11.6	Module A	2	5	38%
Total, 13 families		**6 default, 6 Class I, 1 Class II**	**806.6**				**44%**

Source: scope and classification register (draft; baseline due 18 Dec 2026); Implementing Regulation (EU) 2025/2392; Illustrative

Engineering and notified-body fees drive the EUR 7.9m–11.4m range

Cost driver	Base-case assumption
Programme team	5 FTE × EUR 150k loaded; 2.5 FTE to run
PSIRT	2 extra FTE × EUR 130k, plus EUR 60k on-call allowance
Engineering remediation	26.2 FTE-years × EUR 120k; per family 1.2 default, 2.5 Class I, 4.0 Class II
Shared platforms	EUR 850k build plus EUR 105k run in H2 2027 (EUR 955k one-off); EUR 210k a year to run
Risk assessments	13 families × EUR 45k
Security testing	EUR 35k default / 60k Class I / 90k Class II, per family a year
Documentation	13 families × EUR 40k; EUR 8k per family a year to run
Notified bodies	3 pre-assessments × EUR 20k; 3 Module B × EUR 40k; Module H EUR 115k + 3 × EUR 20k (vendor estimates)
Legal and translations	EUR 180k external legal; 13 × EUR 6k translations
Training, suppliers	EUR 140k training; EUR 90k for 41 in-scope suppliers
Contingency	15% of one-off cost (10% low, 20% high)

Low · EUR 7.9m · EUR 1.76m a year

Standards cited mid-2027; engineering × 0.8, notified-body fees × 0.6, testing × 0.9

Base · EUR 9.3m · EUR 1.84m a year

Plan as assessed at the 28 Oct 2026 baseline

High · EUR 11.4m · EUR 1.90m a year

A second body at premium fees (× 1.6); remediation +30%; a sixth programme FTE; legal × 1.5

Source: Business case and cost model (D10), real 2026 EUR excl. VAT; notified-body fees are vendor estimates, unverified; Illustrative

Twelve terms explain the deck; facts are verified to 30 Oct 2026

CRA
Regulation (EU) 2024/2847: cybersecurity rules for products with digital elements

Harmonised standard
EU standard cited in the Official Journal; applying it presumes conformity

Technical file
Annex VII evidence of conformity, kept 10 years or the support period if longer

SBOM
Software bill of materials: machine-readable component list; not public by default

Product with digital elements
Hardware or software that connects, plus the backends it needs to work

Notified body
Independent assessor designated by a Member State and listed in NANDO

Declaration of conformity (DoC)
Signed statement that a product meets the CRA; needed before CE marking

PSIRT
Product security incident response team: handles vulnerabilities in our products

Class I and Class II
Important product categories in Annex III that need stricter conformity routes

Module A, B+C, H
Internal control; type examination plus conformity to type; full quality assurance

Support period
Period of vulnerability handling: at least five years unless use is shorter

Single Reporting Platform (SRP)
ENISA's portal for Art 14 notifications, live since 11 Sep 2026

Method. Facts verified to 30 Oct 2026 against the engagement knowledge base and an independent fact-check. Guidance C(2026) 5252 is a non-binding approved draft. Client data are illustrative; survey, vendor and commentary figures are labelled by type.

Source: EU Cyber Resilience Act — Engineering Compliance Knowledge Base and fact-check, 30 Oct 2026; EUR-Lex; Commission; ENISA
